



PROPOSITION R

MONTHLY EXECUTIVE UPDATE

PROGRAM UPDATE

AUGUST 13, 2014



FIELD HOUSE CLASSROOM BUILDING

RECEIVING FURNITURE AND EQUIPMENT FOR START OF ACADEMIC YEAR AUGUST 18, 2014

Field House Classroom Building

Accomplished in July

- * Building completed on schedule
- * Reviewing LEED Gold documentation...very close

Planned for August

- * Deliver and install furniture and equipment
- * Grand Opening August 15, 2014
- * First classes August 18, 2014

Wellness Center

Accomplished in July

- ✱ Continuing schematic design and building layout concepts

Planned for August

- ✱ Continue schematic design following District direction for Pool complex



National City Two Story Addition

Accomplished in July

- ✱ Design development completed on schedule
- ✱ District review started

Planned for August

- ✱ Begin collaborative review process with Division of State Architect (DSA)

Solar Initiative Project

Accomplished in July

- ✱ Continue raising panels

Planned for August

- ✱ Complete raising panels
- ✱ Build new switchgear pad
- ✱ Continue coordination for 3 day power outage Labor Day Weekend




Math Science and Engineering

Accomplished in July

- ✱ Continue schematic development

Planned for August

- ✱ Building user group workshop Aug 7th
- ✱ Review proposed floor plans, site plans, etc.

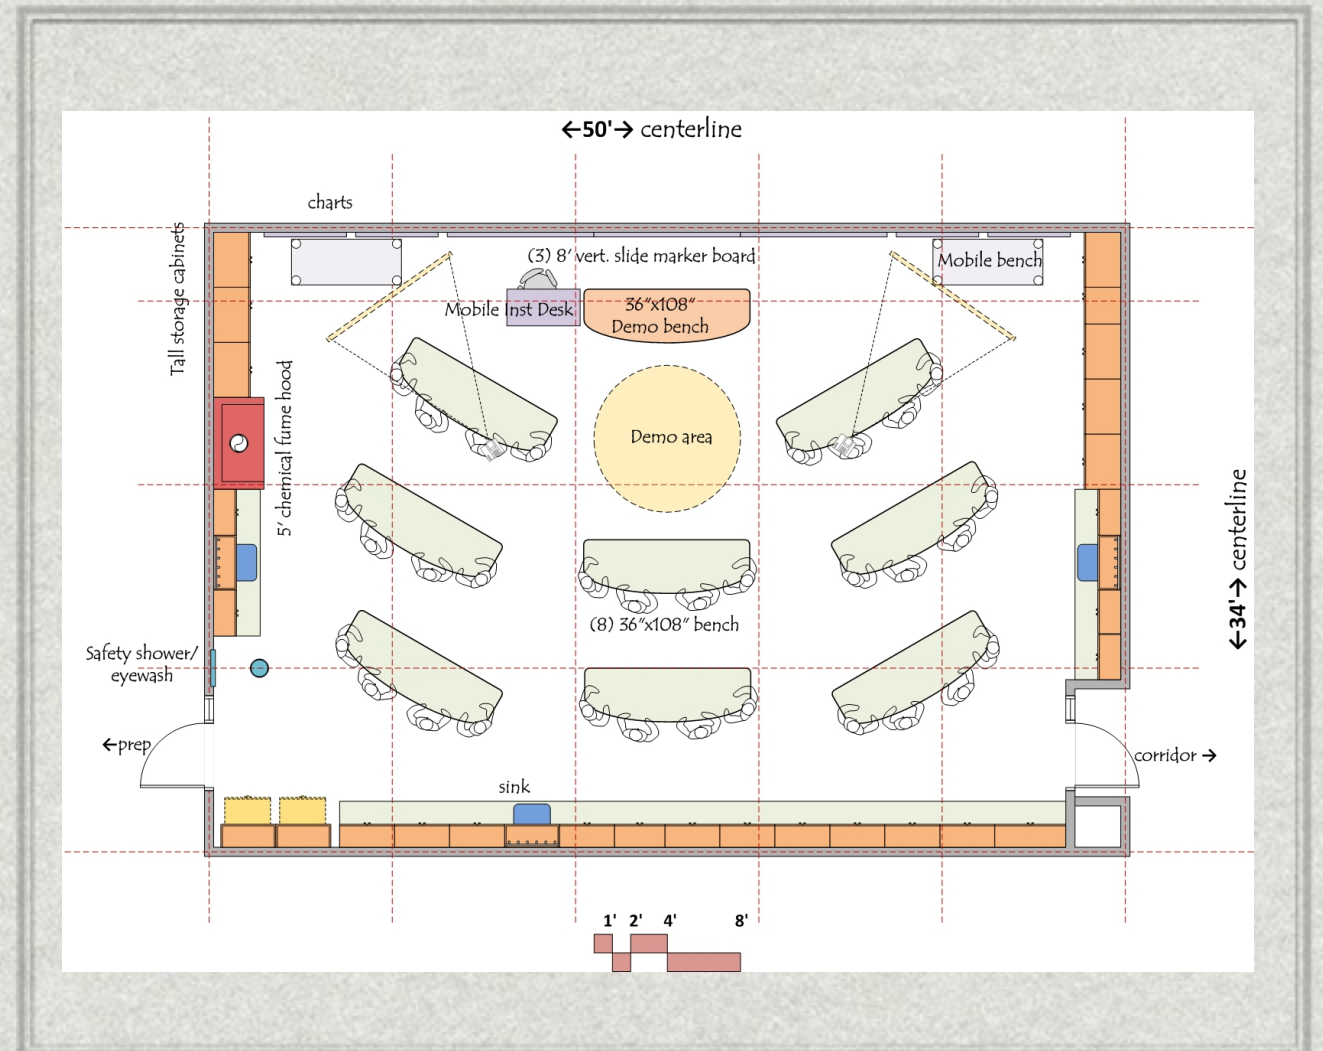

Emergency Communication System

Accomplished in July

- ✱ Received bids


Planned for August

- ✱ Award contract
- ✱ Start work in September



Bond Expenditures

Cumulative Expenditures

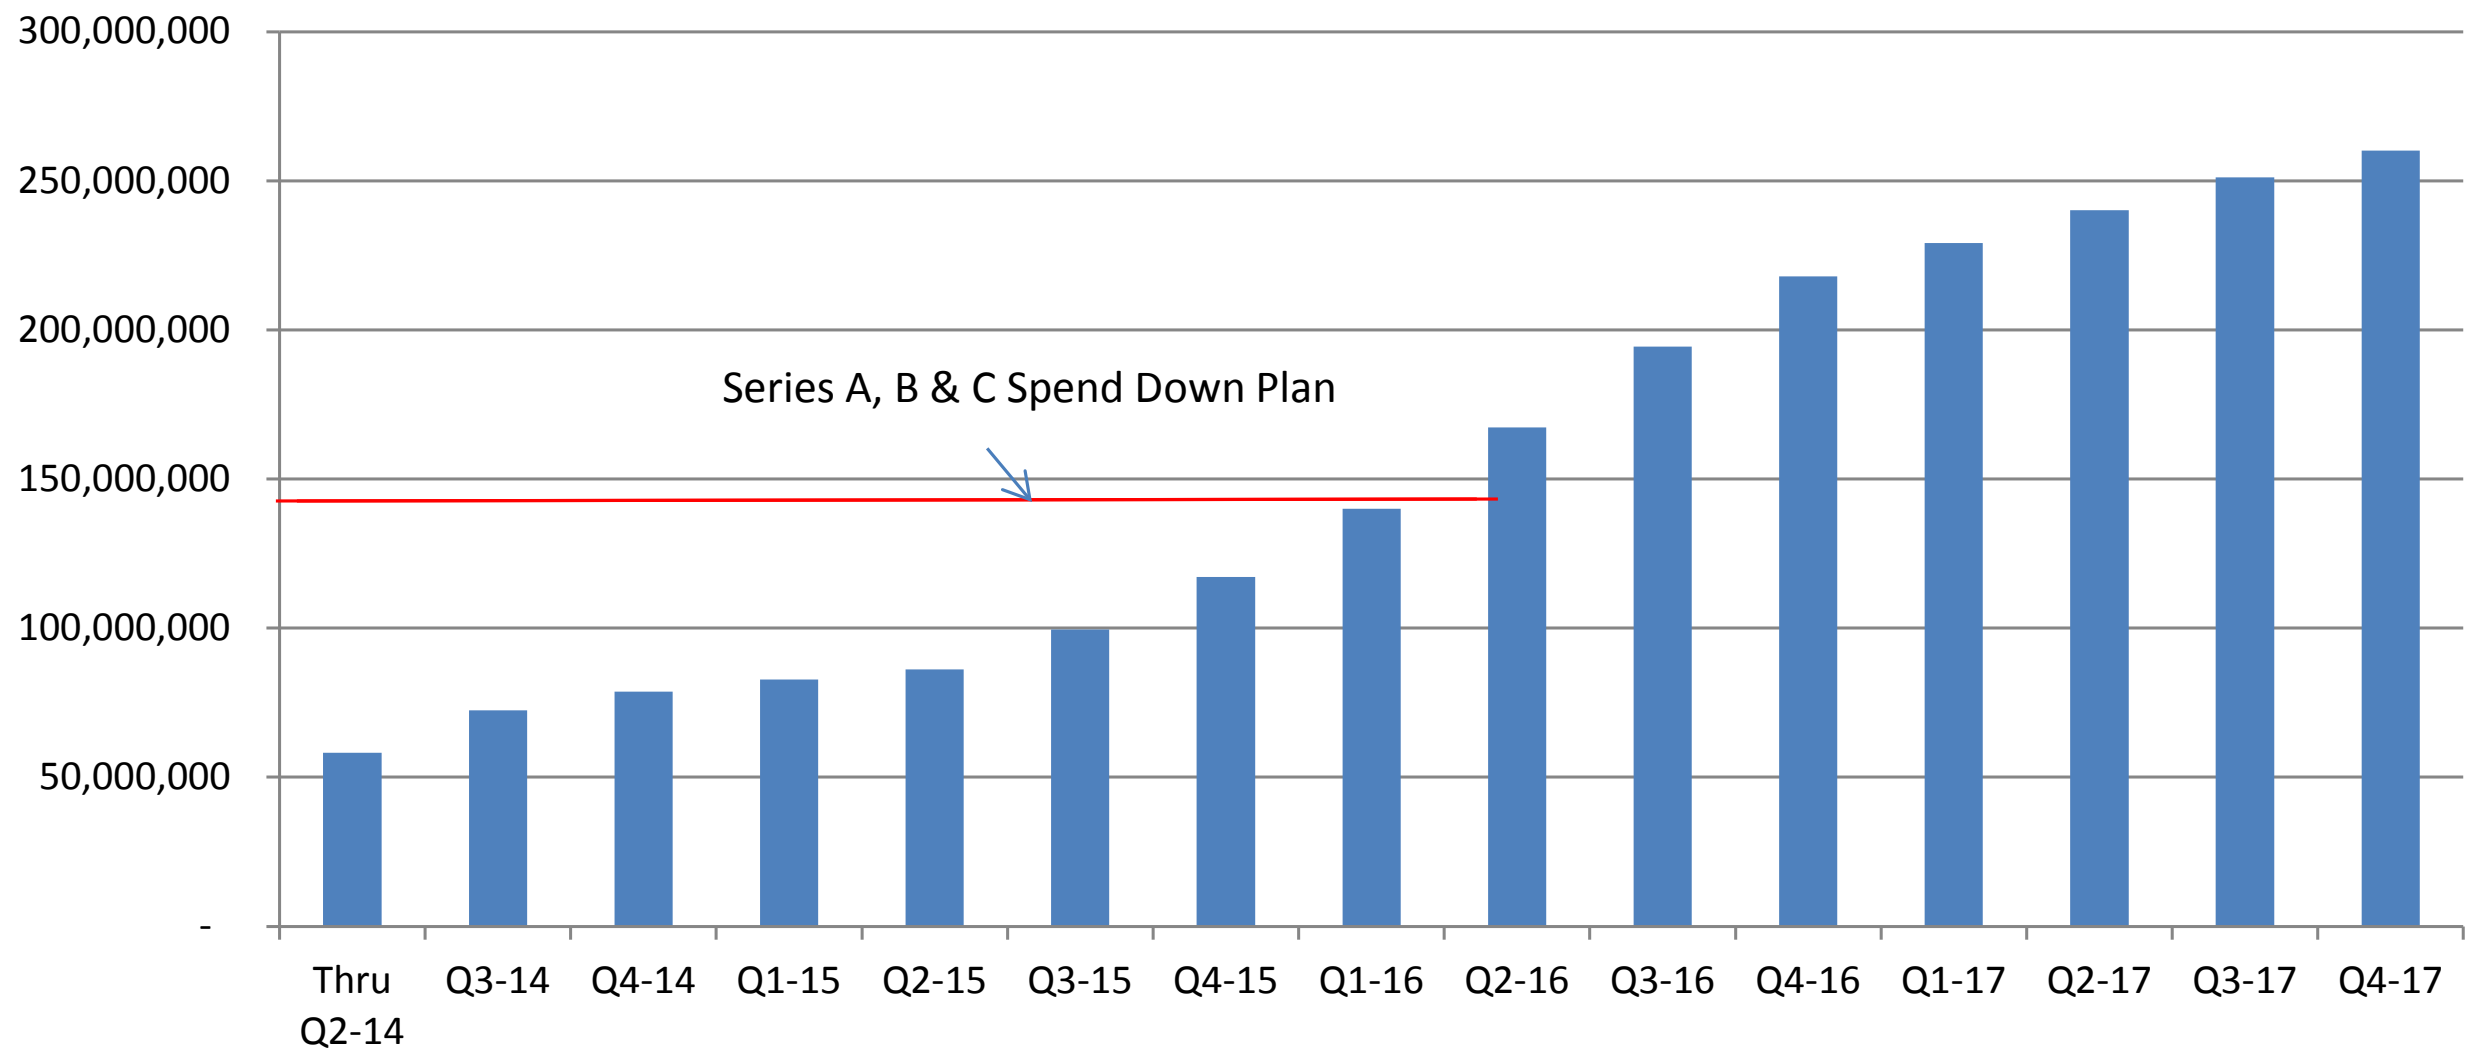



PROPOSITION R
MONTHLY EXECUTIVE UPDATE

PROGRAM UPDATE
AUGUST 13, 2014
