

PROPOSITIONS R & Z EXECUTIVE UPDATE

PROGRAM UPDATE
NOVEMBER 14, 2017

1

National City Addition

Ready for the start of 2018 spring semester

Building interior work nearing completion

 Furniture, Fixtures, and Equipment arriving in December








NATIONAL CITY CLASSROOM BUILDING ADDITION AND BUSINESS CENTER REMODEL

Math, Science, and Engineering Building

Planned completion for start of 2019 spring semester

Demolition of exiting gym beginning winter break
 2017


* Interior metal framing in progress

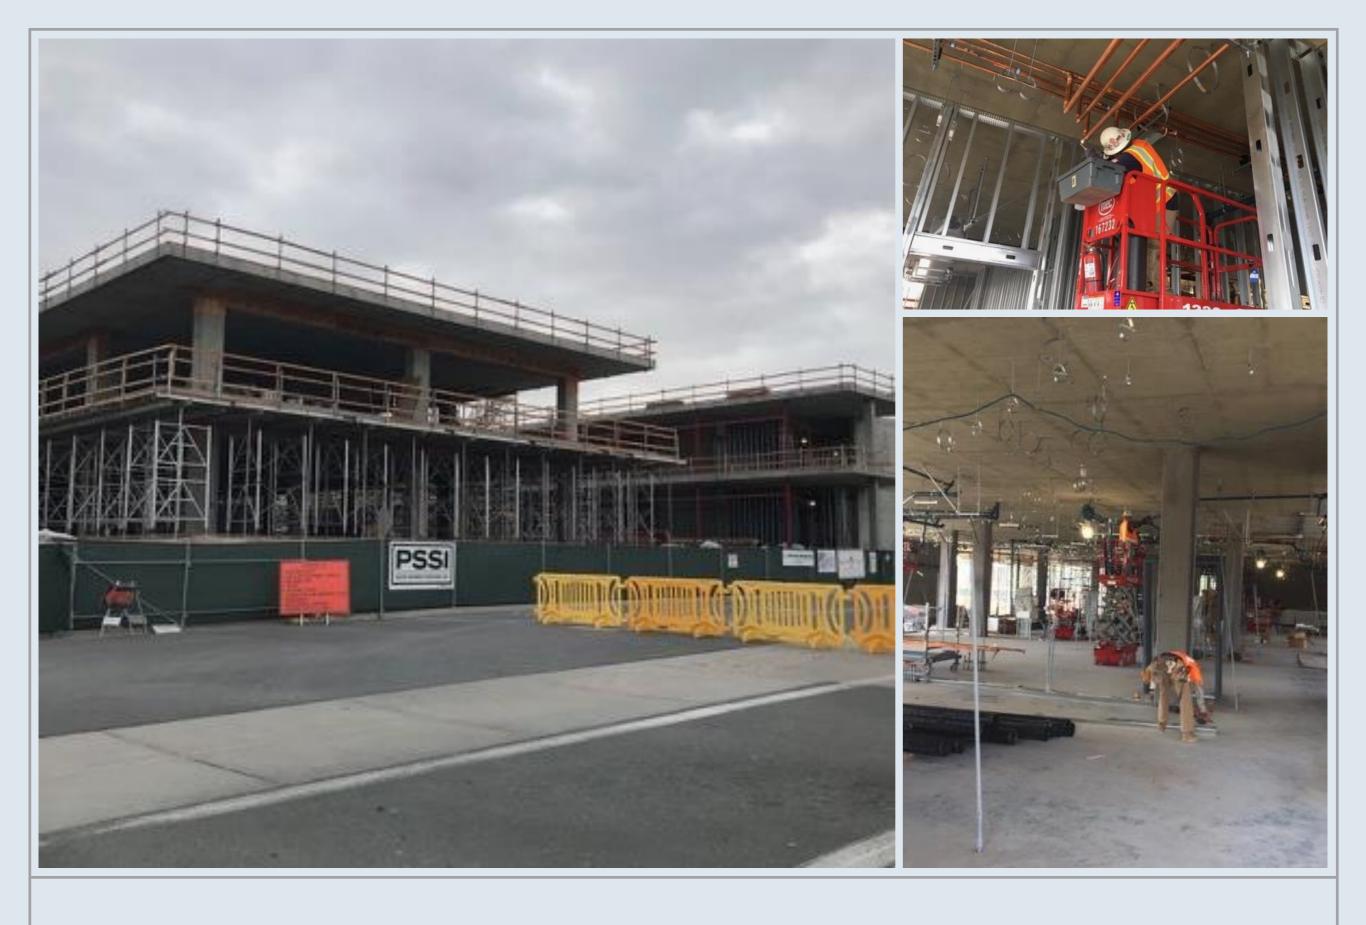

MATH, SCIENCE, AND ENGINEERING BUILDING

Wellness Center and Aquatics Complex

- Ready for start of 2018 spring semester
- Building interior work continuing
- Furniture, Fixtures, and Equipment arriving in December
- Working with Otay Water District on reclaimed water irrigation pipe inspection and approval
- Will push landscaping work into January 2018

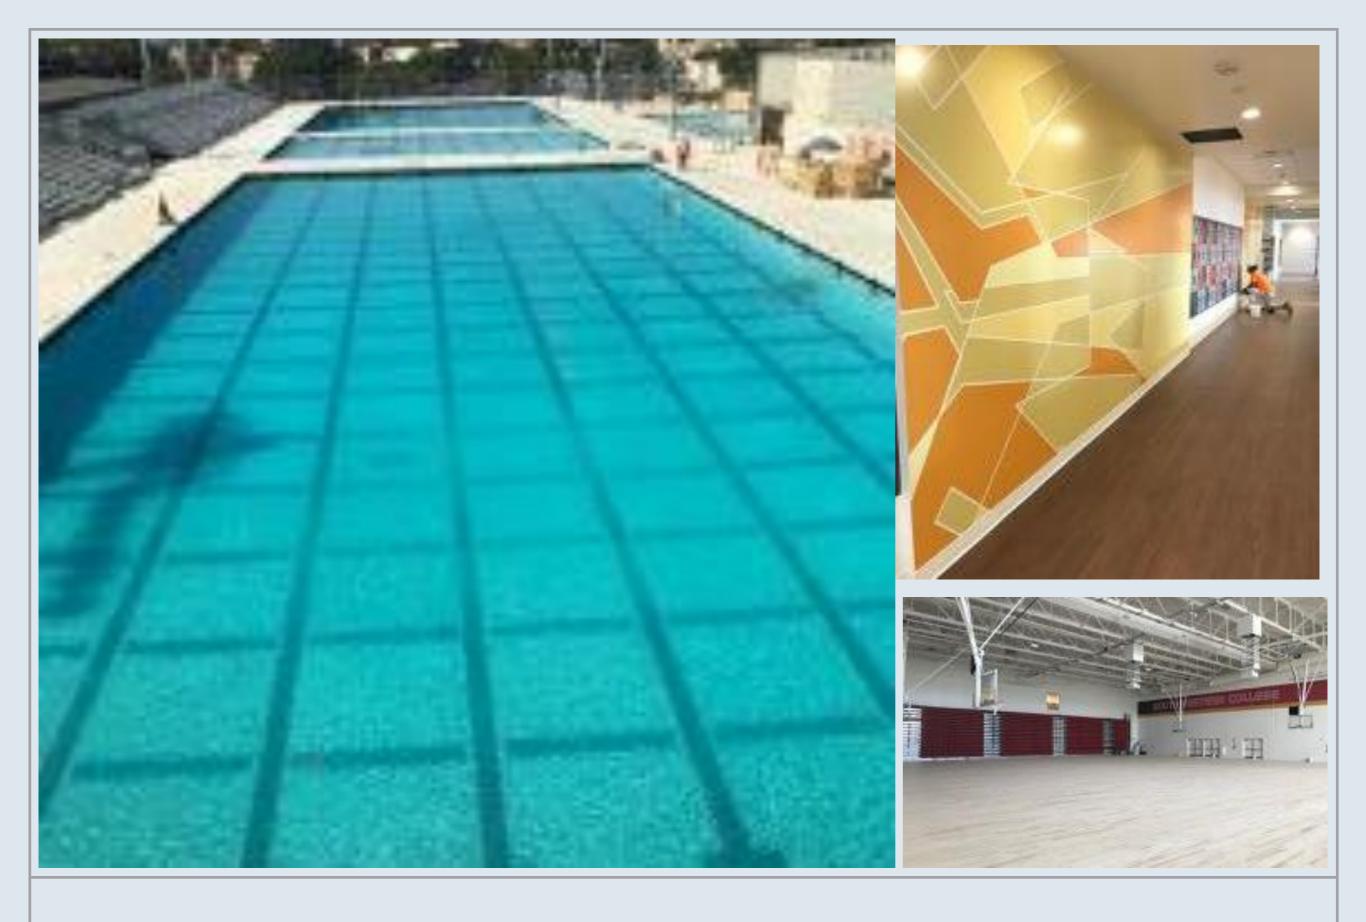

WELLNESS AND AQUATICS COMPLEX

Security Building

- Division of State Architect (DSA) approved the project documents
- A current estimate is being performed by the district consultant
- Network and maintenance departments provided final plans and documents for review
- A project presentation is scheduled for the December Board meeting with a request for approval to proceed with project advertisement

Performing Arts and Cultural Center

- Division of State Architect (DSA) completed review of the project documents for the main building
- * The revised scene construction and storage area is targeted to be approved in late January
- A current estimate is being performed by the district consultant
- * The construction manager at risk is reviewing the main building plans

Utility Infrastructure and Hydronic Piping Project

- Security Building utilities to the project site
- * Emergency power distribution loop from a central emergency generator for buildings requiring this backup system
- * Lighted crosswalk infrastructure
- Communications ducts for network, fire alarm, and building controls
- Completion in December 2017

HEC Otay Mesa Fire Science Project Programming

- * Initial meetings held with the HEC staff
- Quick start is a compliant storage building and options for storing fire trucks (3) and associated equipment
- * Longer term is a facility area to support the Fire Science academic program
- Civil engineers are currently surveying the area and confirming utility capacity






Temporary Parking Area

Secondary Affects of Construction

Performing Arts and Cultural Center
Security Building
Parking Structure

Temporary Parking Area

- Planned for 530 parking spaces
- Replaces spaces lost at O and C lots
- * Includes lighting
- Work planned over the upcoming winter break period
 - Planned bid opening December 7
 - * Request low bid contract ratification to meet this schedule

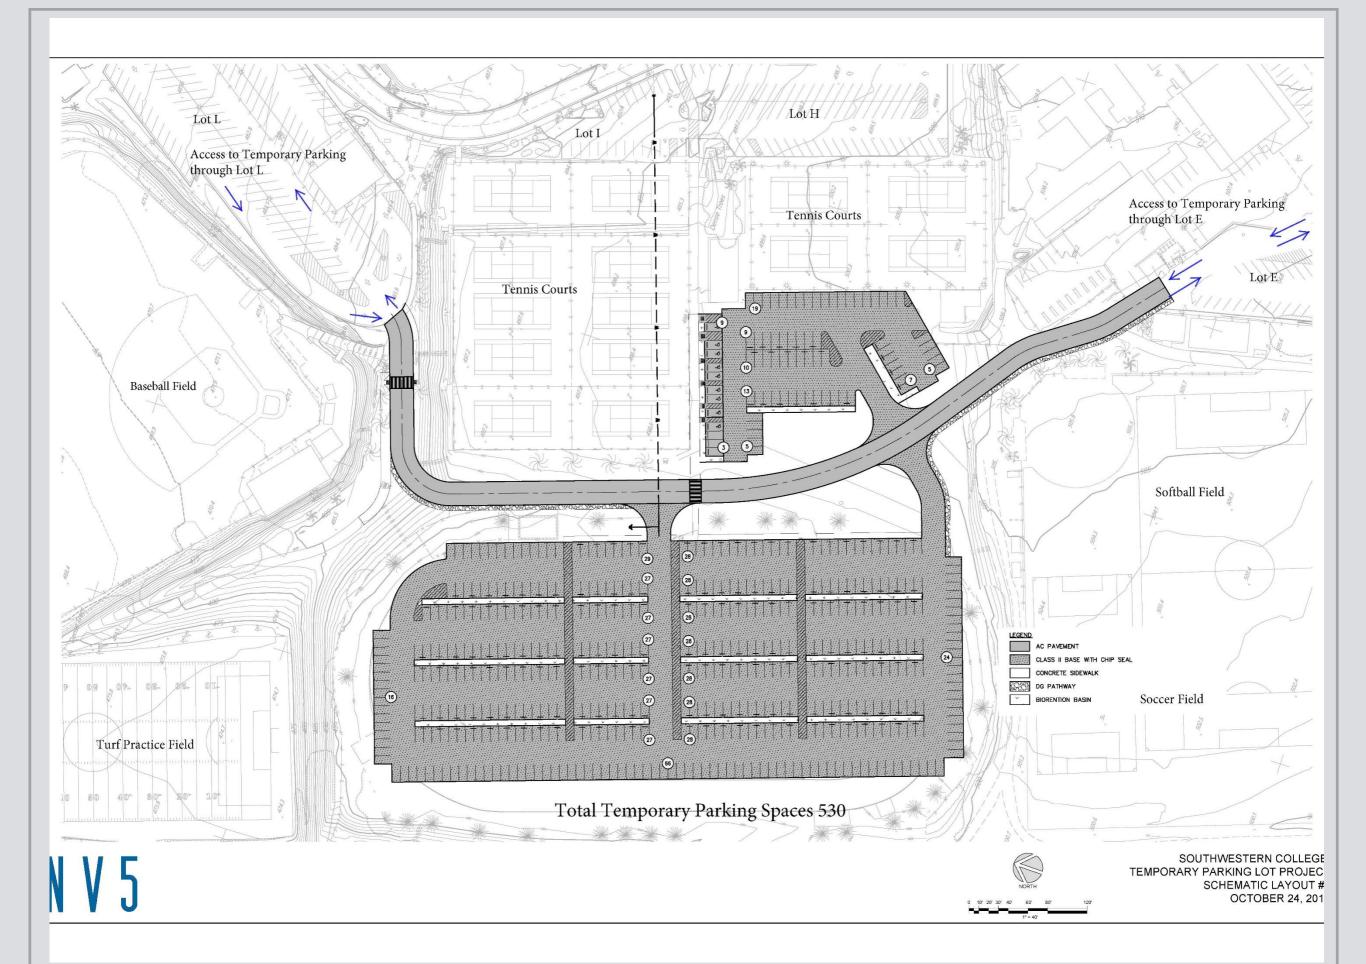

Temporary Parking Area Environmental Planning

- * This temporary parking need is being addressed in an Amendment to Chula Vista Campus Environmental planning document to be presented at the December Board
 - No work on the temporary parking area until the amendment is approved by the Board
- Upon completion of the work in parking lots O and C, the temporary parking area will be restored to the prior use for track and field activities

Parking Structure Update

Parking Structure Overview

- Located in Lot O to serve the needs of the Chula Vista campus
- Planning for 1,000 stalls to replace parking eliminated by construction
- Structure will be ground level and three parking levels above
- * A pedestrian bridge over the ring road will connect the structure to the campus
- * This project will utilize the "Design Build" procurement method


Parking Structure Status

- A request for qualifications was issued and the District received proposals from 7 qualified firms
- A task force was formed to review and evaluate the proposals
- An objective questionnaire was included per the requirements of the California Department of Industrial Relations
- A short list of the 3 highest rated firms was established by the task force at the October 4 meeting:
 - * Bomel Construction Company, Inc.
 - McCarthy Building Companies, Inc.
 - * PCL Construction Services, Inc.

Parking Structure Next Steps

- * A "Design Build" competition to be held using District design criteria
- * The design criteria will be finalized by the project task force:
 - July 19 task force meeting #1
 - September 6 task force meeting #2 with criteria consultants
 - September 15 circulation sub-committee #1 with select criteria consultants
 - September 22 circulation sub-committee #2 with select criteria consultants
 - October 4 tasks force meeting # 3 with criteria consultants
 - October 18 civil/landscape subcommittee meeting #1 with select criteria consultants
 - October 24 Security and IT meeting with select criteria consultants
 - November 8 general task force meeting with the criteria team to discuss and approve final design criteria for inclusion in the RFP
- Issue RFP to the three design build teams

Parking Structure Schedule

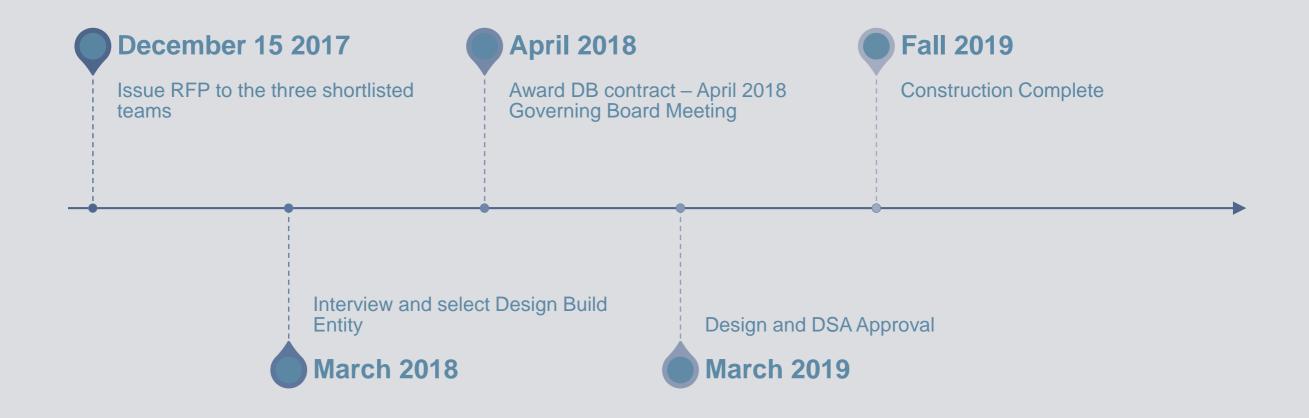


Community Benefits Agreement Local Hire Initiative

LOCAL HIRE INITIATIVE

2016 - 2017 Summary




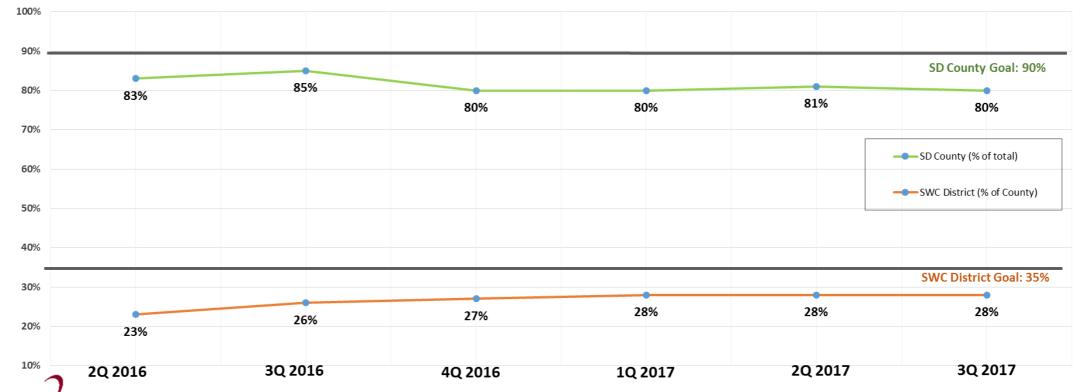


SOUTHWESTERN COLLEGE



LOCAL HIRE INITIATIVE

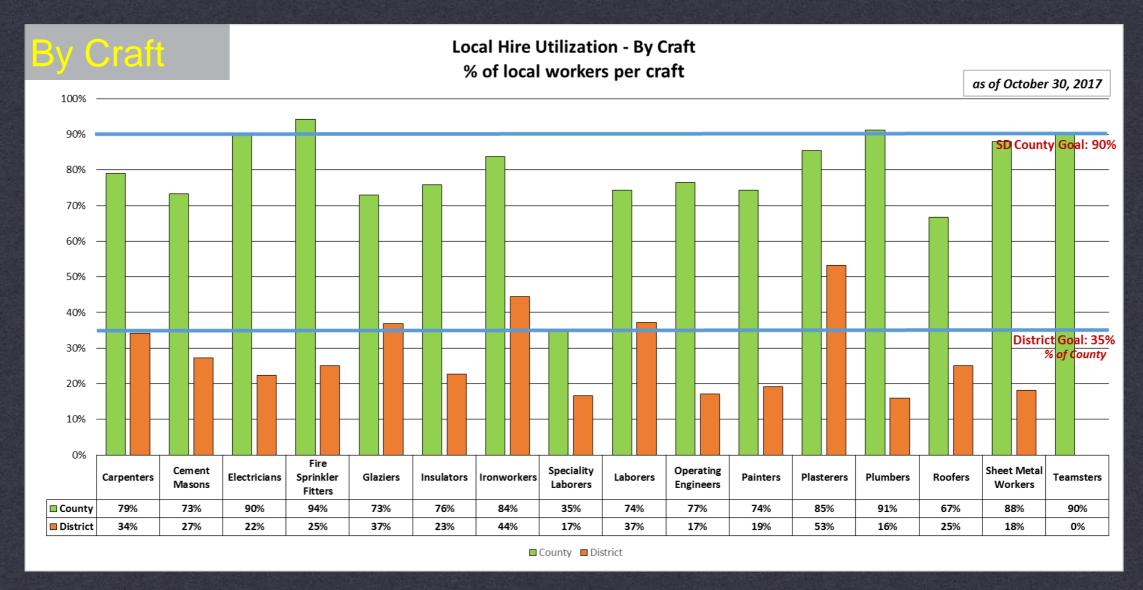

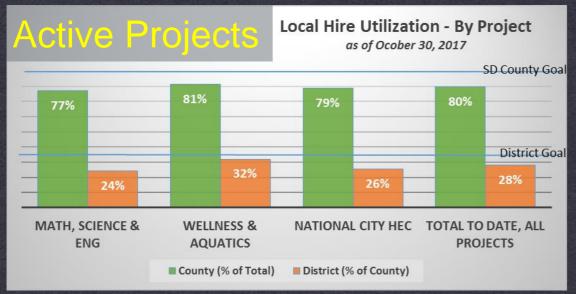

2,176: number of construction related jobs created by Prop R CBA projects and filled by San Diego County residents

613: number of those positions filled by District residents

(all data as of Oct. 30, 2017)



PROPOSITION R & Z EXECUTIVE UPDATE

PROGRAM UPDATE
NOVEMBER 14, 2017
