


SWC IMPLEMENTATION PLAN
CHULA VISTA CAMPUS



PHASE 1 - PROJECTS AERIAL MAP

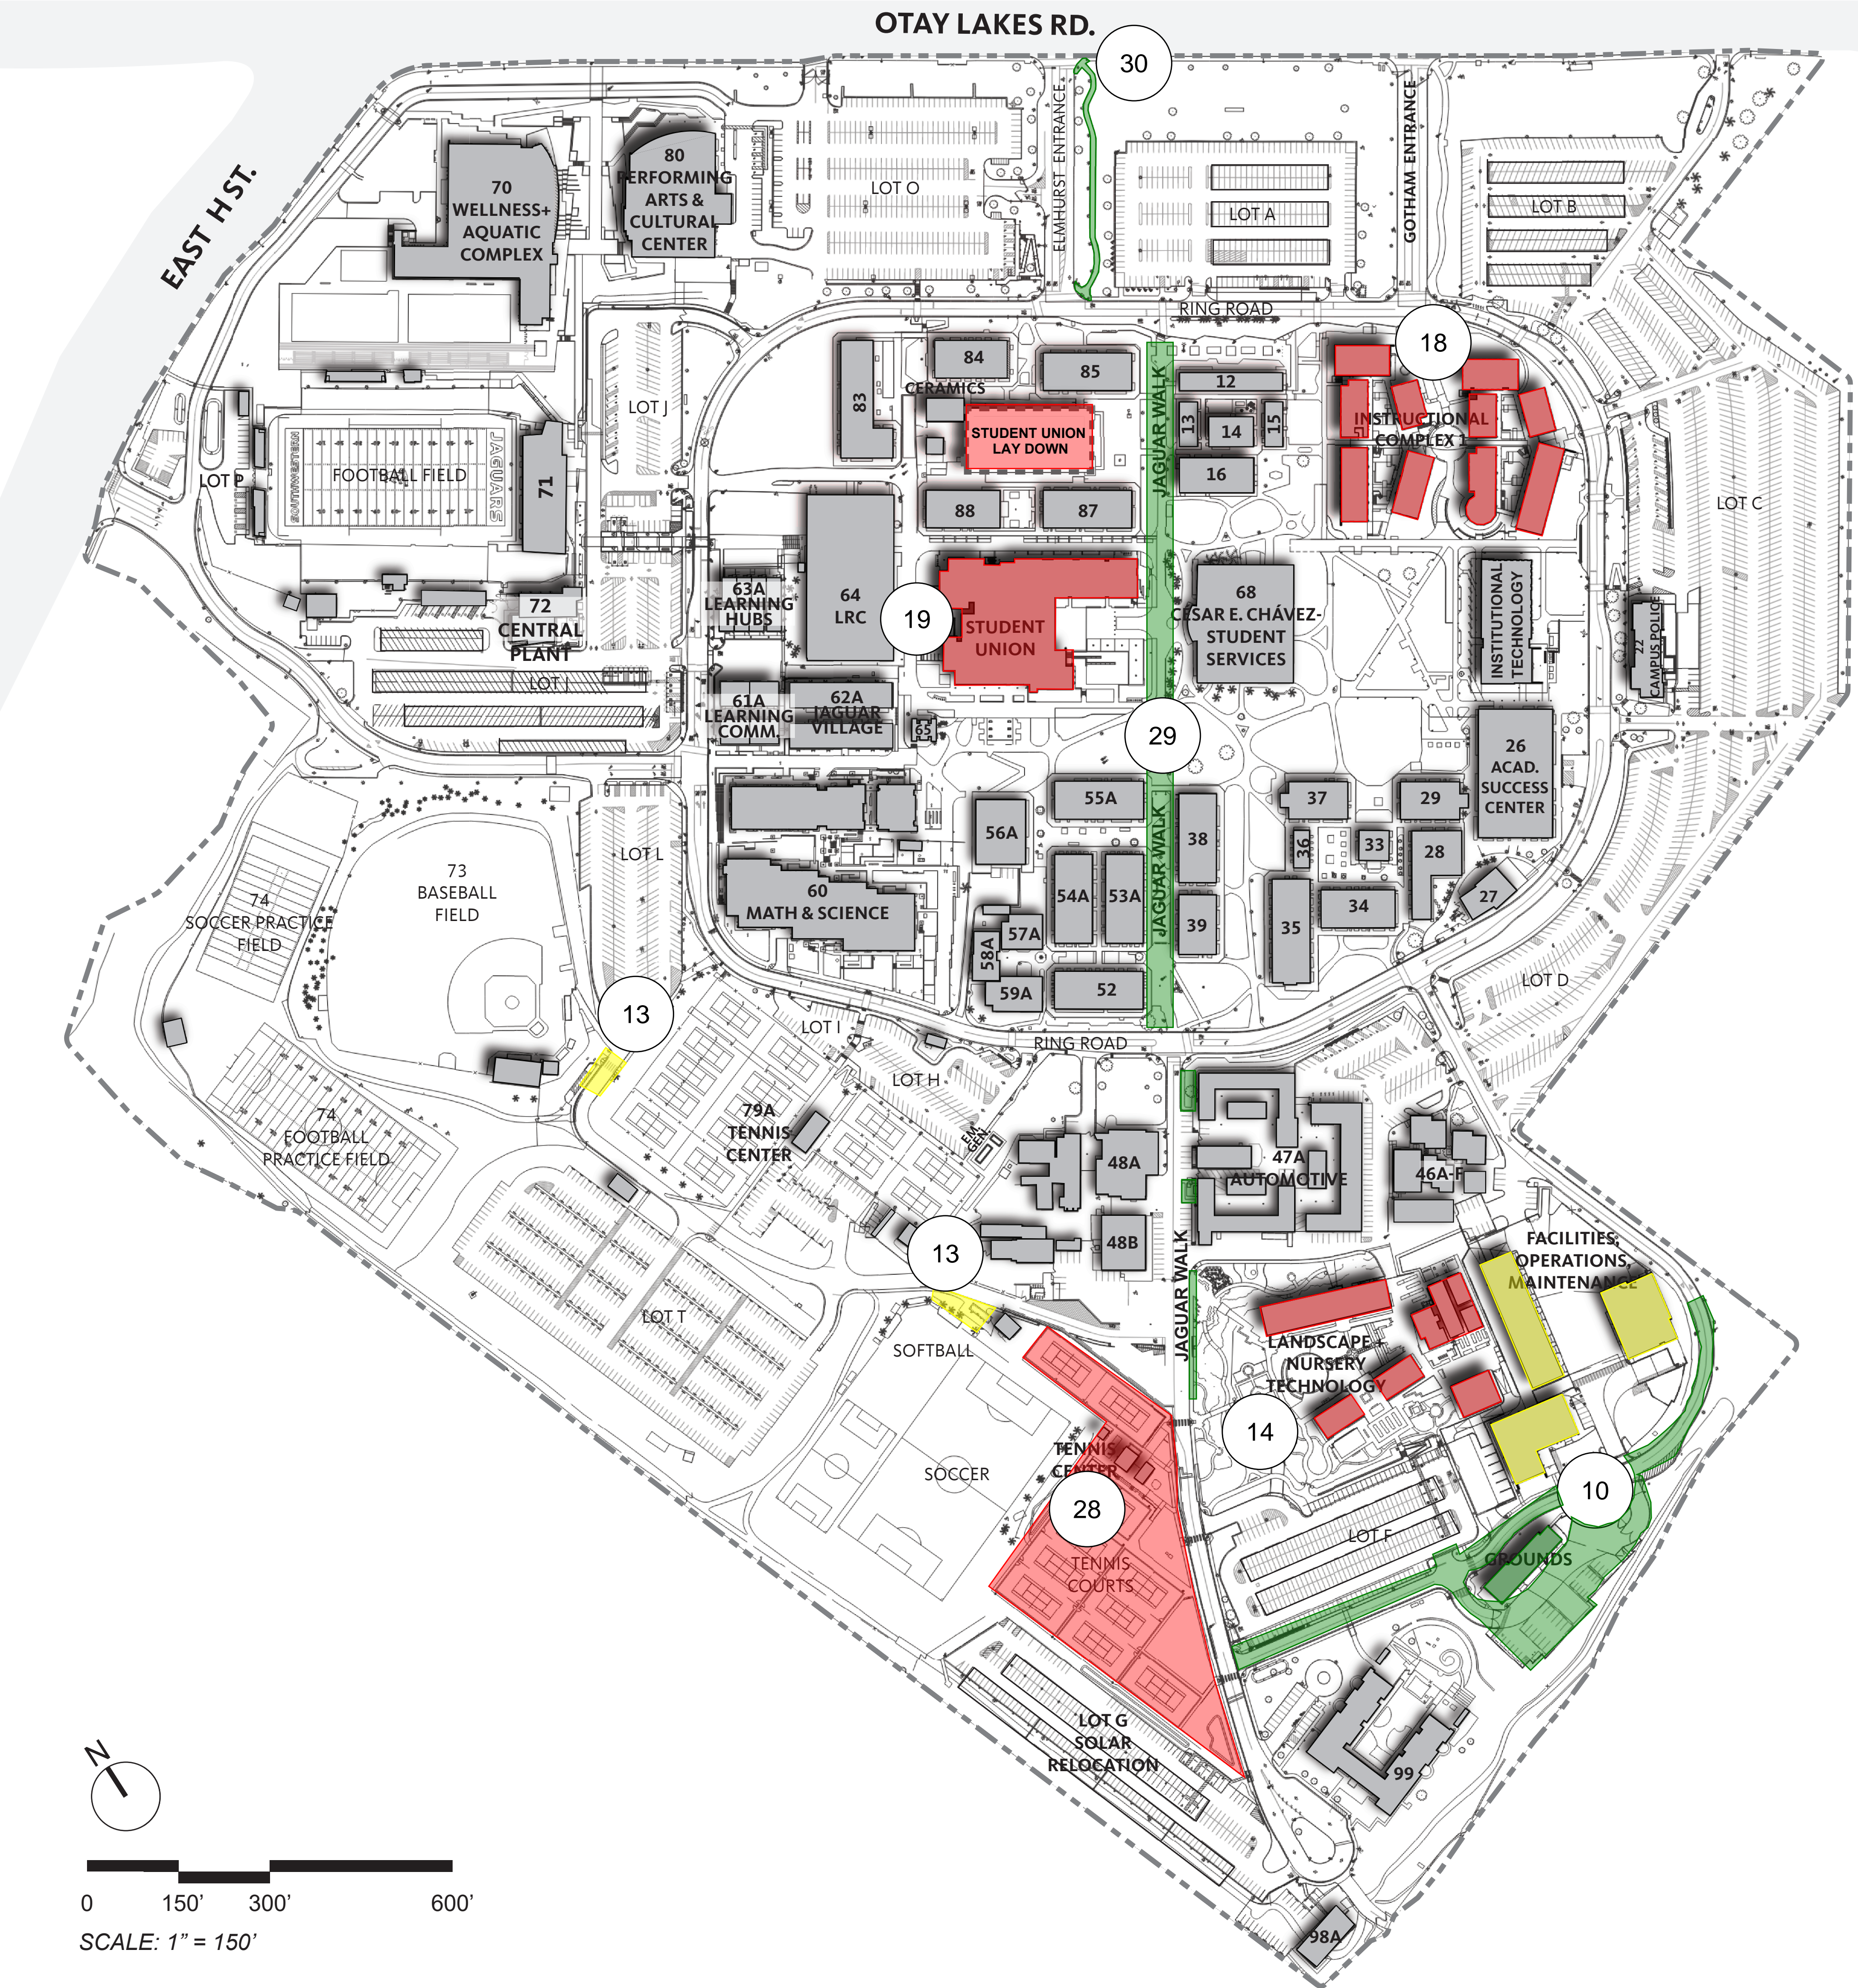

Project Name		Status	Anticipated Start/Finish
10	Operations Warehouse Relocation - Inc 1&2	Completed	Q3 - 2022
	Operations Warehouse Relocation - Inc 3&4	Scheduled	TBD
13	Baseball & Softball Upgrades	Construction	Q4 - 2023
14	Landscape Nursery Technology	Construction	Q2 - 2024
18	Instructional Complex No. 1	Construction	Q1 - 2025
19	Student Union	Construction	Q4 - 2024
28	Tennis Courts	Construction	Q1 - 2024
29	Jaguar Utility Upgrade	Completed	Q1 - 2023
30	Jaguar ADA Upgrade	Completed	Q1 - 2023

