

PROPOSITIONS R & Z EXECUTIVE UPDATE

PROGRAM UPDATE AUGUST 8, 2017

Math, Science and Engineering Building

- Ready for 2019 Spring semester
- Exiting gym demolition targeting December 2017
- Concrete placement continuing



MATH, SCIENCE, AND ENGINEERING BUILDING

National City Addition

- Ready for the start of 2018 Spring semester
- Building interior work at maximum pace
- Exterior siding nearing completion



NATIONAL CITY CLASSROOM BUILDING ADDITION AND BUSINESS CENTER REMODEL

Wellness Center and Aquatics Complex

- Ready for start of 2018 Spring semester
- Building interior work continuing
- Working with SDG&E to minimize delay for energizing the building



WELLNESS AND AQUATICS COMPLEX

Utility Infrastructure and Hydronic Piping Project

- Includes Security
 Building utilities to the project site
- Work continues to planned completion in December 2017



Other Major Facilities Projects

Proposition 39 Clean Energy Projects

- New program funding and new projects in planning
 - Exterior LED lighting Otay Mesa and San Ysidro HEC's
 - Interior LED lighting building 620 (LRC)

Electrical Infrastructure Upgrades

- Phase one complete
- Phase II includes Interior panels, breakers and wiring in 100's, 200's, 850 and 700's buildings



Miscellaneous Projects

- Water resistant landscaping: Work continuing
- HVAC controls: Work continuing
- Fire Alarm Upgrade: Design continuing
- Building 460 roofing: August completion
- Building 470 and 1200 re-roof:
 Planning

- Infrastructure
 - Sewer line and valve replacements: Planning
 - Building structural upgrades: Planning
 - Sidewalk Repair: Planning

Program Level Financial Update

Prop R Bond Financial Overview

- Bond Authorization
- Bond Sales to Date
- Interest to Date
- Total Revenue (Sales + Interest)
- Remaining Authorization (unsold)
 \$ 98.6 million

\$389.0 million \$290.4 million \$ 3.7 million \$394.1 million

Obligations, Encumbrances and Expenditures


- All but \$5 million of the \$294 million in revenue is obligated
- \$261 million has been encumbered (purchase order or contract in place)
- \$184.9 million has been actually spent to date
- \$109.1 million cash on hand

Major Project Expenditures


- DeVore Stadium
- Central Plant
- Technology and Security
- National City HEC Phase II
- Performing Arts Complex
- Wellness and Aquatics Complex
- Solar Initiative
- Math Science and Engineering
- Utilities/Landscape and Entrances
- Management/Misc.
- Total Expenditures

- \$ 33.8 (complete)
- \$ 17.7 (complete)
- \$ 9.9 (complete)
- \$ 17.3 (in progress Spring 2018)
- \$ 3.1 (in progress Requires Prop Z \$)
- \$44.3 (in progress Winter 2017)
- \$ 13.0 (complete)
- \$ 22.0 (in progress Spring 2019)
- \$ 9.0 (complete)
- <u>\$ 14.7</u> \$184.9


Projected Expenditures by Quarter

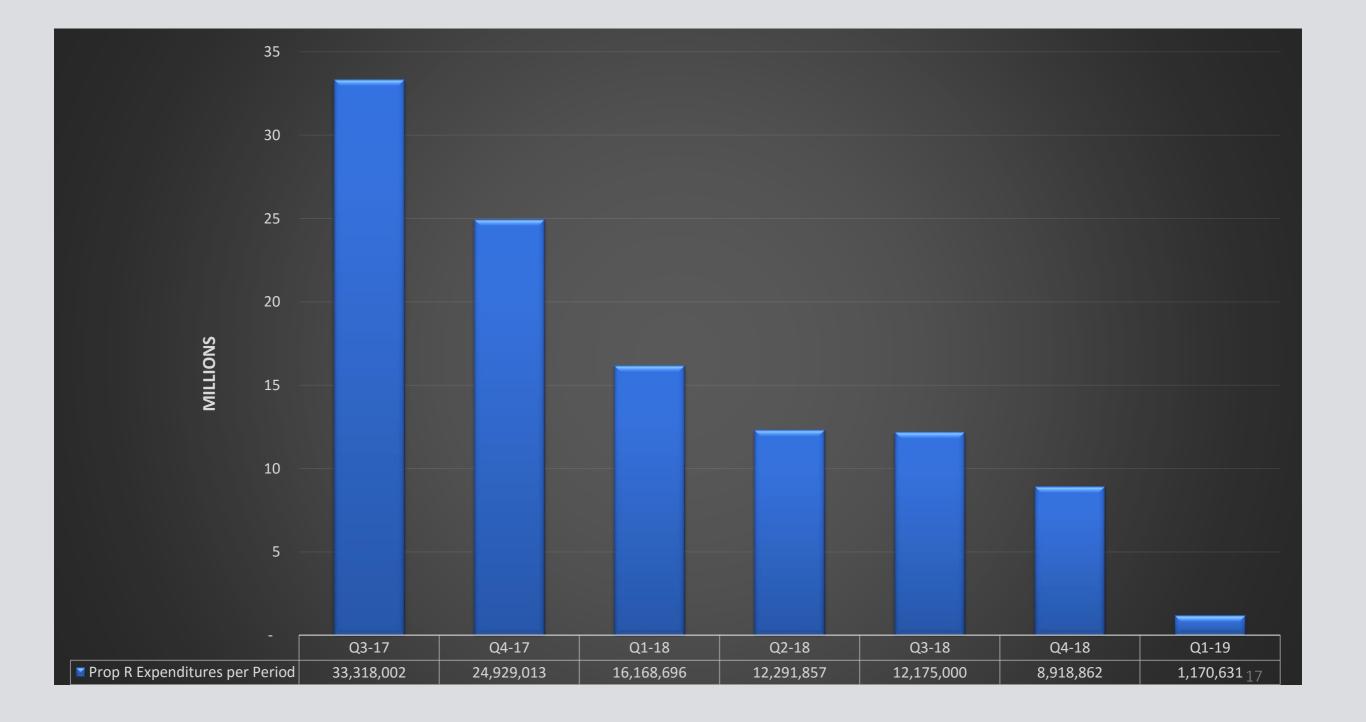

Projected Cash Balance

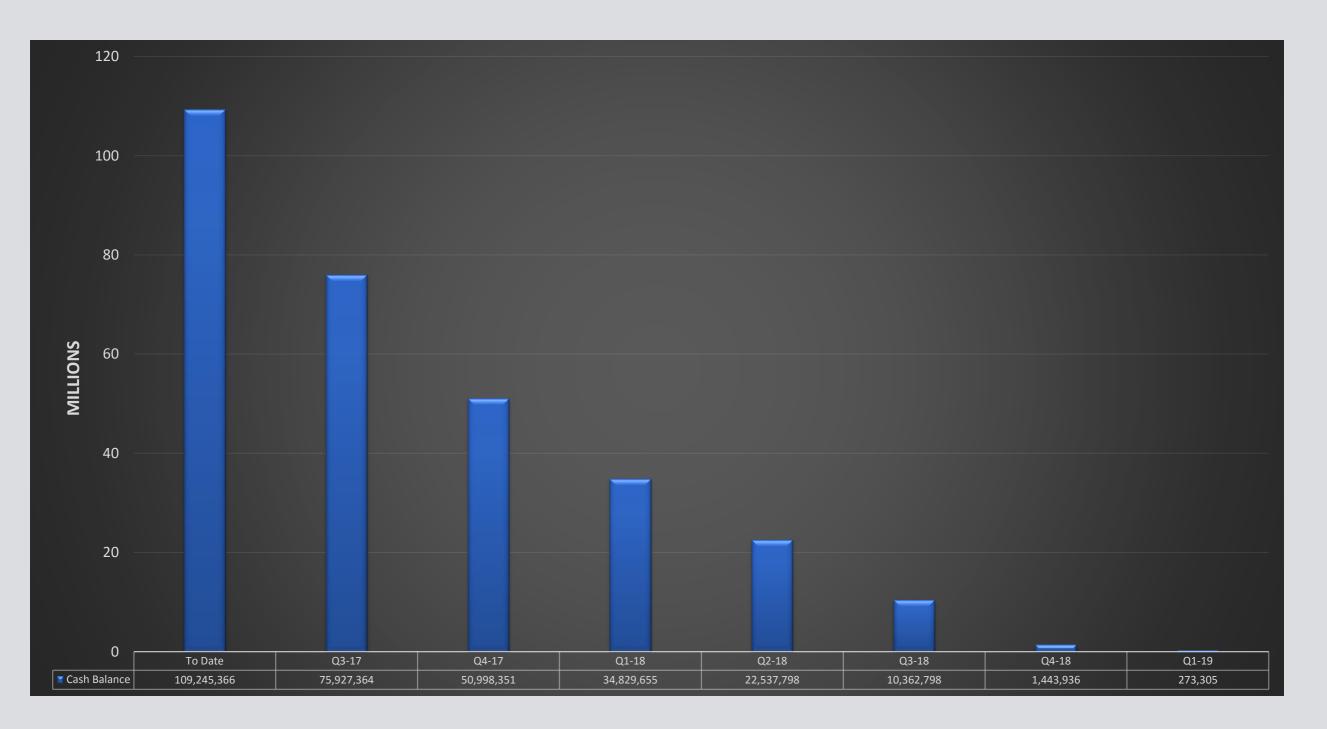

Expenditures per Category

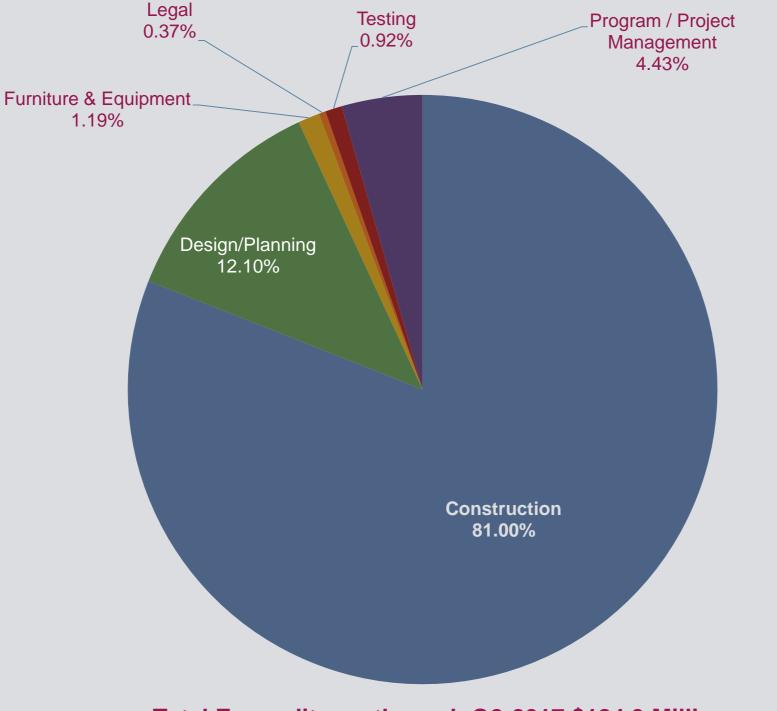


Total Expenditures through Q2-2017 \$184.9 Million

Community Benefits Agreement Local Hire Initiative

LOCAL HIRE INITIATIVE

2Q 2017 By Craft

Local Hire Utilization - By Craft % of local workers per craft

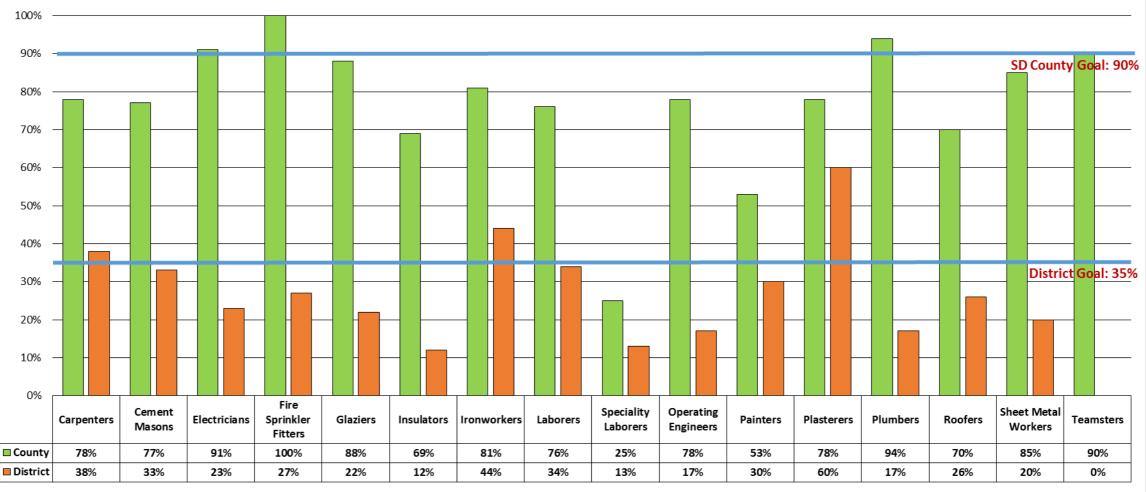

County District


Local Hire Utilization Overall:

- San Diego County: 81%
- District: 28%

LOCAL HIRE INITIATIVE

2016 - 2017 Summary

CBA Local Hire Utilization 2016-2017

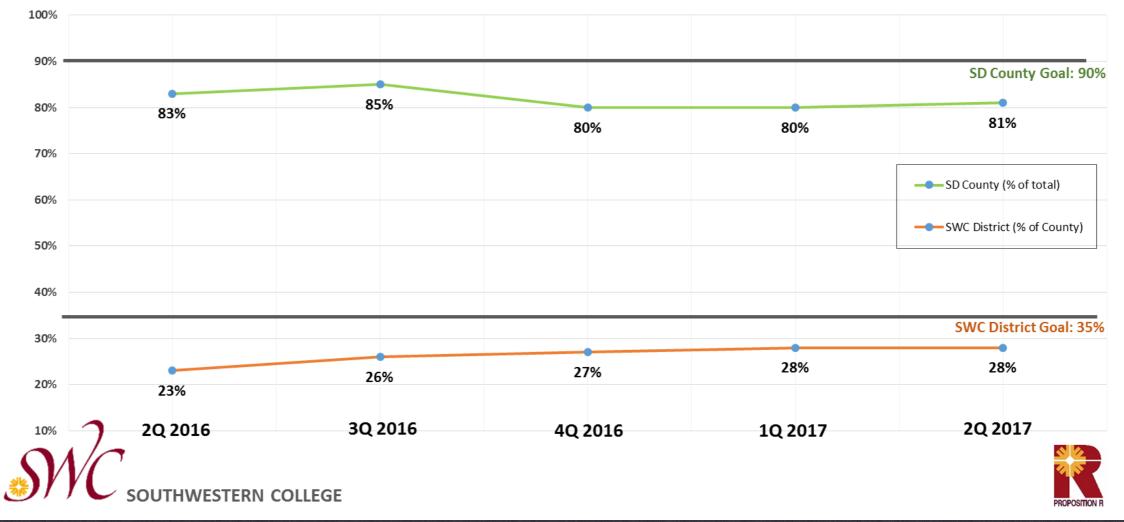



PROPOSITION R & Z EXECUTIVE UPDATE

PROGRAM UPDATE AUGUST 8, 2017
