SWC 2018 FMP Schedule

Proposition R & Z

May 2022 Update

Activity ID	Activity Name	Start	Finish
Southwestern Community College District		03-Sep-18 A	23-Nov-24
Phase 1 Projects		03-Sep-18 A	23-Nov-24
Student Union		10-Aug-20 A	06-Nov-23
1A	Planning	10-Aug-20 A	01-Mar-21 A
1B	Project Programing	02-Mar-21 A	11-Jun-21 A
2A	Design	14-Jun-21 A	26-Aug-21 A
2C	DSA	02-Aug-21 A	28-Feb-22 A
3A	Bid	11-May-22 A	26-Jun-22 A
4A	Award	29-Jun-22 A	28-Aug-22
5A	Construction	29-Aug-22	22-Sep-23
5C	Substantial Completion		22-Sep-23
5D	FF&E	23-Sep-23	07-Oct-23
5E	Move Users In	03-Oct-23	07-Oct-23
6A	Close Out	08-Oct-23	06-Nov-23
Baseball & Softball Upgrades		17-Sep-19 A	07-Mar-23
1A	Planning	17-Sep-19 A	17-Sep-19 A
1B	Project Programing	17-Sep-19 A	01-Aug-21 A
2A	Design	18-Jan-21 A	28-Nov-21 A
2C	DSA	21-Aug-21 A	08-May-22 A
3A	Bid	19-Jul-22*	21-Sep-22
4A	Award	22-Sep-22	22-Sep-22
5A	Construction	22-Sep-22	05-Feb-23
5C	Substantial Completion		05-Feb-23
6A	Close Out	06-Feb-23	07-Mar-23
Moran Hall Demolition		02-Jan-20 A	14-Oct-22
1A	Planning	02-Jan-20 A	13-Apr-20 A
2A	Design	14-May-20 A	13-Jun-21 A
2C	DSA	15-Nov-20 A	26-Oct-21 A
3A	Bid	01-Aug-21 A	20-Sep-21 A
4A	Award	20-Sep-21 A	26-Oct-21 A
5A	Construction	06-Dec-21 A	15-Aug-22
5C	Substantial Completion		15-Aug-22
6A	Close Out	16-Aug-22	14-Oct-22
Campus-Wide Trellis Repairs		01-Nov-21 A	01-Mar-23
1A	Planning	01-Nov-21 A	15-Nov-21 A
1B	Project Programing	16-Nov-21 A	30-Nov-21 A
2A	Design	01-Dec-21 A	03-Feb-22 A
2C	DSA	14-Feb-22 A	14-Jul-22
3A	Bid	15-Jul-22	12-Sep-22
4A	Award	13-Sep-22	22-Sep-22
5A	Construction	23-Sep-22	30-Jan-23
5C	Substantial Completion		30-Jan-23
6A	Close Out	31-Jan-23	01-Mar-23
Fire Alarm Upgrades		06-Jan-20 A	22-Sep-22
1A	Planning	06-Jan-20 A	23-Mar-20 A
1B	Project Programing	23-Mar-20 A	31-Mar-20 A
2A	Design	01-Apr-20 A	08-Oct-20 A
2C	DSA	01-Jul-20 A	01-Aug-21 A
3A	Bid	19-Oct-20 A	08-Dec-20 A
5A	Construction	09-Dec-20 A	28-Jul-22
6A	Close Out	24-Aug-22	22-Sep-22
Ceramic Relocation		03-Jan-22 A	20-Jul-22
1A	Planning	02-Jan-20 A	01-Aug-20 A
1B	Project Programing	02-Aug-20 A	02-Sep-20 A
2A	Design	03-Sep-20 A	01-Aug-21 A
3A	Bid	04-Sep-20 A	01-Aug-21 A
5A	Construction	14-Oct-20 A	30-Jun-22
6A	Close Out	01-Jul-22	20-Jul-22
Sewer Line and Path of Travel		22-Apr-20 A	21-Oct-22
1A	Planning	22-Apr-20 A	02-Nov-20 A
1B	Project Programing	22-Jun-20 A	02-Nov-20 A
2A	Design	03-Nov-20 A	24-Mar-21 A
2C	DSA	10-Jan-21 A	01-Aug-21 A
3A	Bid	25-Mar-22 A	29-Apr-22 A
4A	Award		29-Apr-22 A
5A	Construction	31-May-22 A	20-Oct-22
5C	Substantial Completion		20-Oct-22
6A	Close Out	21-Oct-22	21-Oct-22
Building 16 Renovation (Building 14/16)		01-Aug-19 A	04-Apr-23
1A	Planning	01-Aug-19 A	20-Sep-19 A
1B	Project Programing	01-Aug-19 A	27-Sep-19 A
2A	Design	30-Sep-19 A	28-Dec-20 A
2C	DSA	28-Dec-20 A	28-Dec-21 A
5A	Construction	08-Aug-22*	03-Feb-23
5C	FF&E	04-Feb-23	05-Mar-23
6A	Close Out	06-Mar-23	04-Apr-23
Tennis Courts		01-Sep-19 A	15-Feb-24
1A	Planning	01-Sep-19 A	08-Nov-19 A
1B	Project Programing	11-Nov-19 A	30-Dec-19 A
2A	Design	31-Dec-19 A	10-Nov-21 A
2C	DSA	11-Nov-21 A	13-May-22 A
3A	Bid	07-Nov-22*	05-Jan-23
4A	Award	06-Jan-23	25-Jan-23
5A	Construction	26-Jan-23	21-Aug-23
6A	Close Out	22-Aug-23	15-Feb-24
Instructional Complex #1		04-Aug-20 A	18-Sep-24
1A	Planning	04-Aug-20 A	01-Feb-21 A
1B	Project Programing	02-Feb-21 A	25-May-21 A
2A	Design	02-Nov-21 A	02-May-22 A
2C	DSA	30-May-22 A	26-Jun-22
3A	Bid	19-Apr-22 A	17-May-22 A
4A	Award (Includes CBA/Alignment)	18-May-22 A	09-Jul-22
5A	Construction	20-Jul-22*	14-Aug-24
5C	Substantial Completion		13-Aug-24
5D	FF&E	15-Aug-24	13-Sep-24
5E	Move Users In	25-Aug-24	13-Sep-24
6A	Close Out	15-Aug-24	18-Sep-24
Landscape + Nursery Technology		01-Nov-18 A	23-Nov-24
1A	Planning	01-Nov-18 A	11-Jun-19 A
1B	Project Programing	01-Nov-18 A	11-Jun-19 A
2A	Design	11-Jun-19 A	24-May-22 A
2C	DSA	01-Jul-22 A	11-Jul-22
3A	Bid #3	01-Aug-22*	29-Sep-22
4A	Award	30-Sep-22	19-Oct-22
5A	Construction	20-Oct-22	19-Dec-23
5C	Substantial Completion		19-Dec-23
5D	FF&E	20-Dec-23	17-Apr-24
5E	Move Users In	18-Apr-24	27-Apr-24
6A	Close Out	28-Apr-24	23-Nov-24
Building 710 Electrical Relocation		05-Aug-19 A	27-Aug-22
1A	Planning	02-Jan-20 A	13-Oct-20 A
1B	Project Programing	02-Jan-20 A	01-Aug-21 A
2A	Design	05-Aug-19 A	02-Oct-20 A
5A	Construction	13-Oct-20 A	28-Jul-22
6A	Close Out	29-Jul-22	27-Aug-22
Jaguar Village		03-Sep-18 A	07-Sep-22
1A	Planning	03-Sep-18 A	12-Nov-19 A
1B	Project Programing	13-Nov-19 A	06-Dec-19 A
2A	Design	09-Dec-19 A	31-Jan-20 A
2C	DSA	02-Aug-21 A	28-Sep-21 A
3A	Bid	15-Dec-21 A	19-Jan-22 A
4A	Award		19-Jan-22 A
5A	Construction	23-Feb-22 A	08-Aug-22
5C	Substantial Completion		08-Aug-22
6A	Close Out	09-Aug-22	07-Sep-22
IT Data Center		02-Aug-19 A	10-Sep-22
1A	Planning	04-Aug-19 A	12-Nov-19 A
1B	Project Programing	02-Aug-19 A	05-Aug-19 A
2A	Design	05-Aug-19 A	03-Aug-20 A
2C	DSA	03-Aug-20 A	31-Jan-21 A
3A	Bid	31-Jan-21 A	19-Jul-21 A
4A	Award	20-Jul-21 A	20-Jul-21 A
5A	Construction	21-Jul-21 A	22-Jul-22
5C	Substantial Completion		22-Jul-22
5D	FF&E	23-Jul-22	11-Aug-22
5E	Move Users In	07-Aug-22	11-Aug-22
6A	Close Out	12-Aug-22	10-Sep-22
Operations and Warehouse Relocation		01-Nov-18 A	10-May-23
1A	Planning	01-Nov-18 A	28-Dec-18 A
1B	Project Programing	02-Jan-19 A	13-Jun-19 A
2A	Design	14-Mar-19 A	02-Jul-20 A
2C	DSA	29-Aug-19 A	02-Jul-20 A
3A	Bid	01-Mar-21 A	15-Jun-21 A
4A	Award	23-Aug-21 A	23-Aug-21 A
5A - 1	Construction Increment 1	26-Aug-21 A	10-Jan-23
5A - 2	Construction Increment 2	23-Aug-21 A	23-Oct-22
5C	Substantial Completion		10-Jan-23
5D	FF&E	11-Jan-23	11-Mar-23
6A	Close Out	12-Mar-23	10-May-23

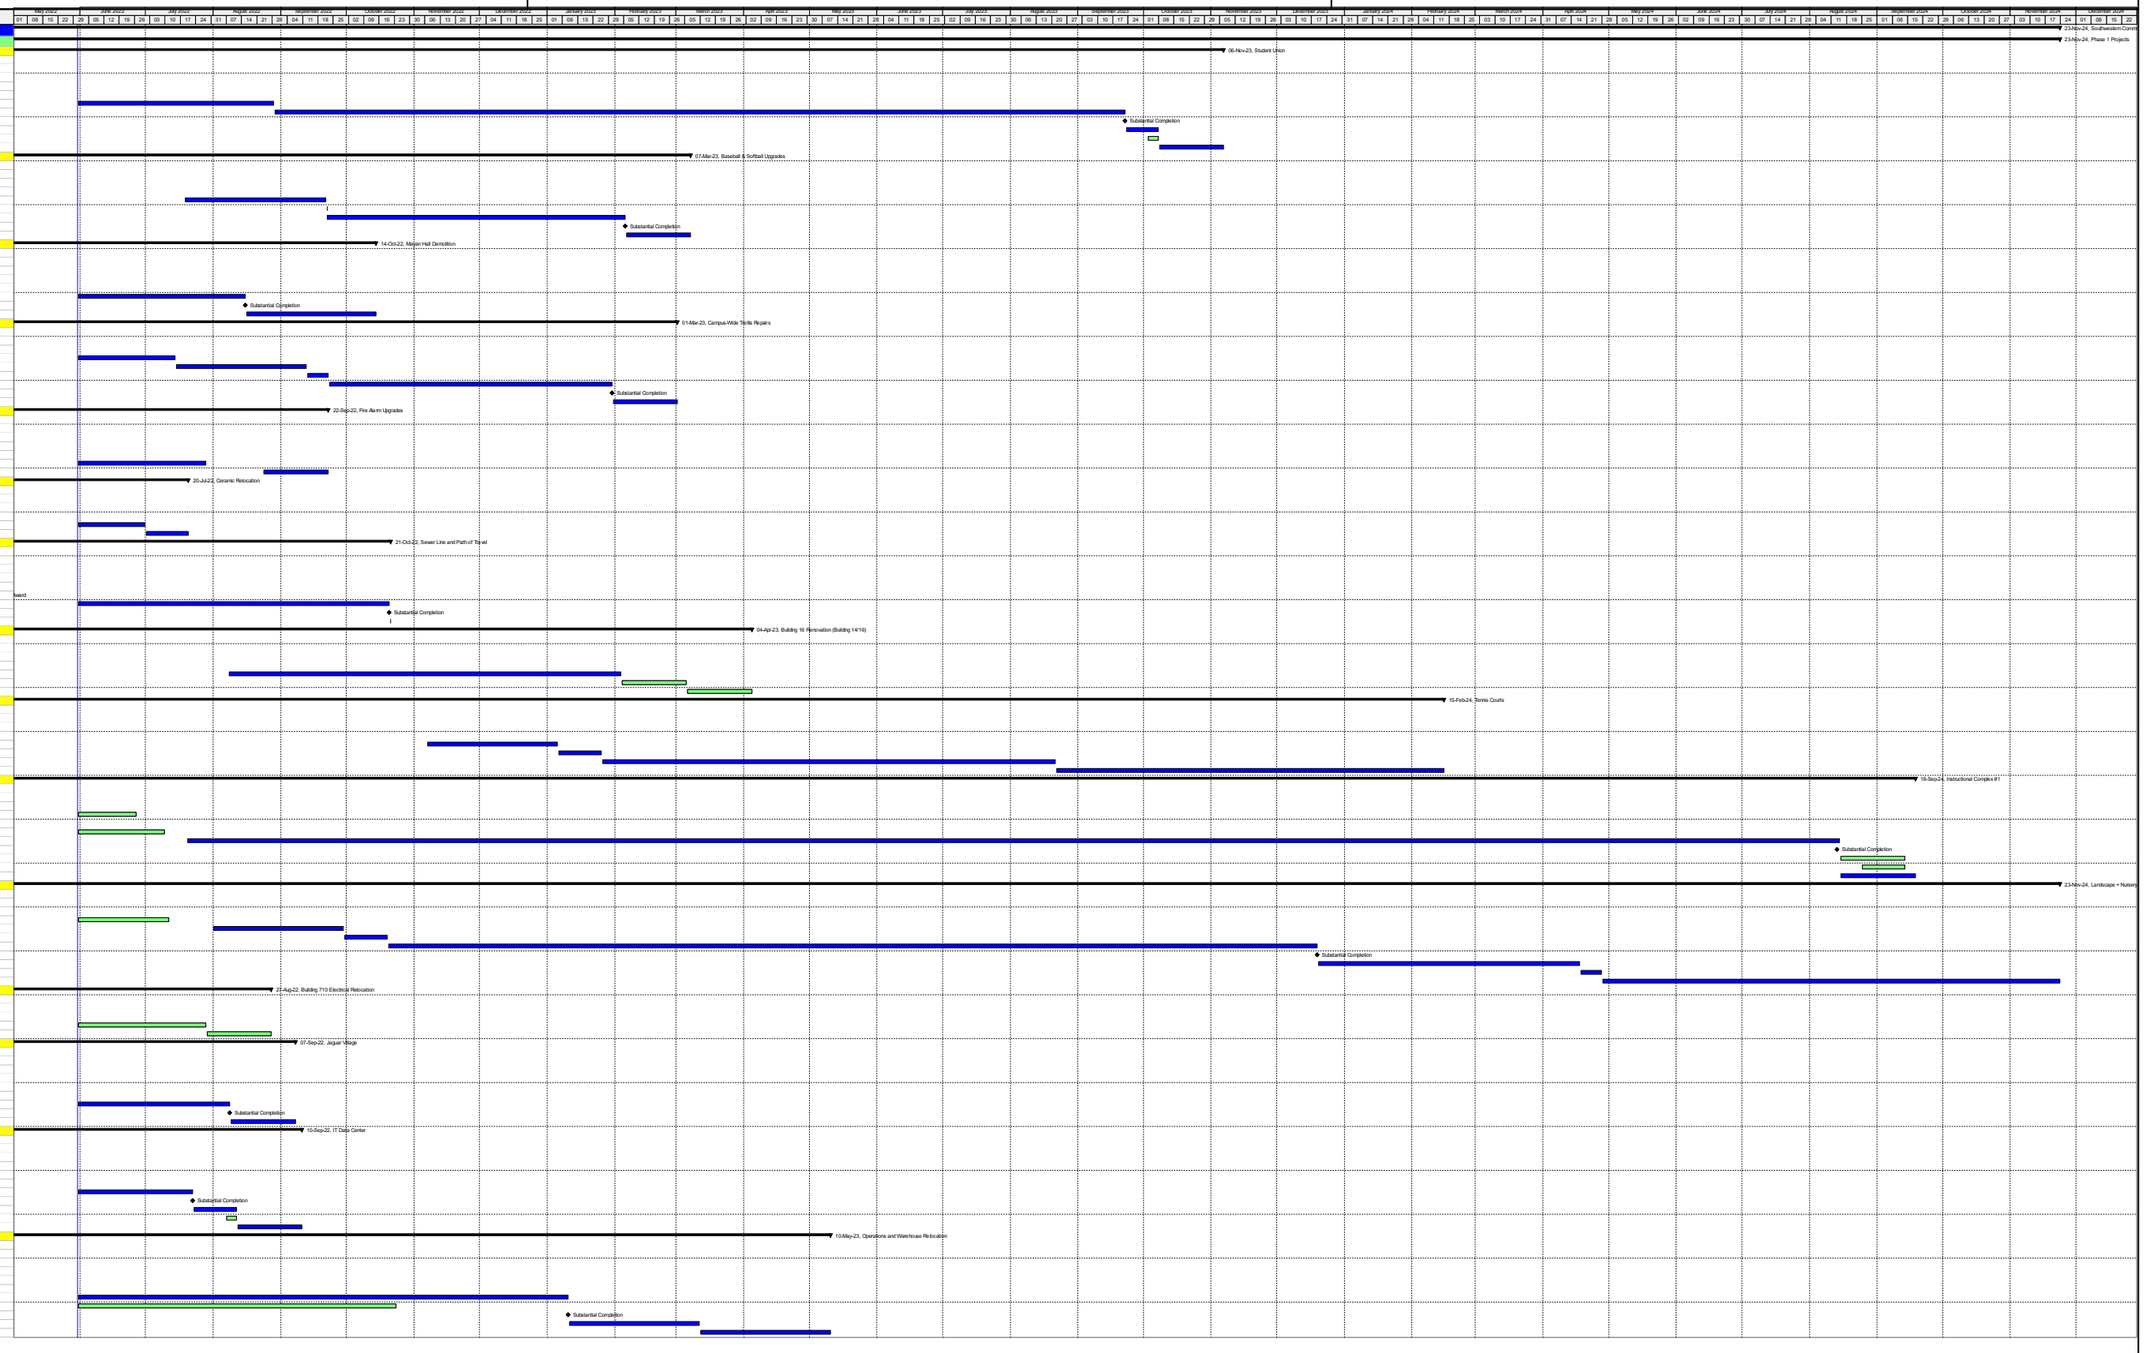

Actual Work ◆ Milestone

Remaining Work Summary

Schedular: Mike Carmichael - mcarmichael@swccd.edu
