Activity Name	Original Duration	Start	Finish
SWC FMP 2018 Projections April 2021	1868	23-Apr-18 A	11-Sep-24
Phase 1 Projects	1868	23-Apr-18 A	11-Sep-24
B2100D Performing Arts Center (CMR)	1155	23-Apr-18 A	30-Jul-21
Procurement	10	23-Apr-18 A	21-Jul-18 A
Construction	850	22-Jul-18 A	01-May-21
Close-out	91	01-May-21	30-Jul-21
FF&E	60	02-May-21	30-Jun-21
Occupy	0		30-Jun-21
Wayfinding	773	01-Aug-18 A	29-Dec-20 A
Design	140	01-Aug-18 A	18-Dec-18 A
DSA Approval	120	19-Dec-18 A	17-Apr-19 A
Procurement	90	18-Apr-19 A	16-Jul-19 A
Construction	420	17-Jul-19 A	29-Dec-20 A
Otay Mesa Higher Education Center	1777	23-Apr-18 A	20-Oct-22
Otay Mesa Public Safety Training Center (CMR)	877	23-Apr-18 A	31-Aug-21
Project Kick-off	0	23-Apr-18 A	
Programming	60	23-Apr-18 A	21-Jun-18 A
Design	330	22-Jun-18 A	17-May-19 A
DSA Approval	171	18-May-19 A	04-Nov-19 A
Procurement	90	05-Nov-19 A	02-Feb-20 A
Board Approval	0		11-Feb-20 A
Construction	450	12-Feb-20 A	02-Aug-21
FF&E	15	02-Aug-21	16-Aug-21
Close-out	30	02-Aug-21	31-Aug-21
Occupy	0		16-Aug-21
Otay Mesa Auto Shop (CMR)	1304	01-Jan-19 A	25-Jul-22
Project Kick-off	0	01-Jan-19 A	
Programming	107	01-Jan-19 A	17-Apr-19 A
Design	221	07-Feb-20 A	02-Nov-20 A
DSA Approval	120	03-Nov-20 A	03-May-21
Procurement	60	04-May-21	02-Jul-21
Construction	360	03-Jul-21	27-Jun-22
FF&E	30	28-Jun-22	27-Jul-22
Occupy	0		27-Jul-22
Close-out	90	28-Jul-22	25-Oct-22
Parking/Site Development (CMR)	1000	10-Feb-20 A	15-Aug-23
Planning	80	10-Feb-20 A	27-Apr-20 A
DSA Approval	90	29-Apr-20 A	21-Aug-20 A
Procurement	60	04-Sep-20 A	10-Nov-20 A
Construction	120	20-Dec-20	18-Apr-21
Campus Infrastructure	1597	06-Jan-20 A	31-Dec-21
Fire Alarm Upgrades	1207	06-Jan-20 A	21-May-21
Project Kick-off	0	06-Jan-20 A	
Programming	20	07-Jan-20 A	31-Mar-20 A
Design	120	01-Apr-20 A	30-Jun-20 A
DSA Approval	120	01-Jul-20 A	08-Oct-20 A
Procurement	90	10-Oct-20 A	08-Dec-20 A
Construction	165	09-Dec-20 A	21-May-21
Lower Life Repairs/Path of Travel (CMR)	1347	22-Apr-20 A	31-Dec-21
Project Kick-off	0	22-Apr-20 A	
Programming	30	23-Apr-20 A	02-Nov-20 A
Design	40	03-Nov-20 A	10-Jan-21 A
DSA Approval	30	10-Jan-21 A	24-Mar-21 A
Procurement	76	25-Mar-21	08-Jun-21
Construction	177	08-Jul-21	31-Dec-21
Access Controls	1022	22-Apr-20 A	19-Mar-21 A
Project Kick-off	0	22-Apr-20 A	
Programming	30	23-Apr-20 A	01-Jul-20 A
Design	40	02-Jul-20 A	03-Aug-20 A
Procurement	30	10-Aug-20 A	13-Oct-20 A
Construction	20	19-Oct-20 A	19-Mar-21 A
Lighting Controls	1020	22-Apr-20 A	19-Mar-21 A
Project Kick-off	0	22-Apr-20 A	
Programming	30	23-Apr-20 A	01-Jul-20 A
Design	40	02-Jul-20 A	03-Aug-20 A
Procurement	30	10-Aug-20 A	13-Oct-20 A
Construction	136	14-Oct-20 A	19-Mar-21 A
Butler / Tennis Court Relocation	1118	01-Sep-19 A	13-Oct-27
Tennis Relocation	1118	01-Sep-19 A	11-Jun-21
Project Kick-off	0	01-Sep-19 A	
Programming	69	01-Sep-19 A	08-Nov-19 A
Design	80	12-Nov-19 A	30-Jan-20 A
DSA Approval	35	31-Jan-20 A	05-Mar-20 A
Procurement/Buyout/Fabrication	102	19-Feb-20 A	29-Sep-20 A
COVID-19 Delay	75	29-Apr-20 A	25-Sep-20 A
Mobilize	2	28-Sep-20 A	29-Sep-20 A
Remove Existing	28	30-Sep-20 A	30-Oct-20 A
Survey	5	02-Nov-20 A	10-Nov-20 A
Install Foundation Bases	16	11-Nov-20 A	30-Nov-20 A
Install New System	77	01-Dec-20 A	30-Apr-21
Commissioning and Closeout	40	30-Apr-21	11-Jun-21
Lot G Demo (Soils Stockpile)	90	18-Jun-21	30-Jun-21
Design	20	18-Jun-21*	06-Feb-21
Procurement	60	07-Feb-21	07-Apr-21
Demo	60	08-Apr-21	06-Jun-21
Grounds Demolition	180	20-Sep-21	18-Mar-22
Design	60	20-Sep-21	18-Nov-21
Demolition	120	19-Nov-21	18-Mar-22
Tennis Courts and Facilities	691	11-Nov-19 A	12-Oct-22
Programming	50	11-Nov-19 A	30-Dec-19 A
Design	144	31-Dec-19 A	07-Jun-21 A
DSA Approval	168	08-Jun-21	24-Jun-21
Procurement	60	18-Jun-22	18-Mar-22
Construction	268	19-Mar-22	12-Oct-22
Ceramics/Bldg. 710 Yard Relocation/Demo Mayan Hall (CMR)	740	02-Jun-20 A	30-Nov-21
Mayan Hall Demolition (CMR)	372	02-Jun-20 A	30-Nov-21
Planning	260	02-Jun-20 A	24-Feb-21 A
Procurement	76	25-Feb-21	11-May-21
Construction	154	30-Jun-21	30-Nov-21
Ceramics Relocation	180	02-Jun-20 A	30-May-21
Planning	260	02-Jun-20 A	03-Sep-20 A
Procurement	90	04-Sep-20 A	13-Oct-20 A
Construction	180	14-Oct-20 A	30-May-21
Bldg. 710 Electrical Yard Relocation	180	02-Jun-20 A	30-May-21
Planning	260	02-Jun-20 A	03-Sep-20 A
Procurement	90	04-Sep-20 A	13-Oct-20 A
Construction	180	14-Oct-20 A	30-May-21
Bldg 14 and 16 Remodel (1600s Demo)	1355	01-Aug-19 A	16-Apr-25
Programming	60	01-Aug-19 A	29-Sep-19 A
Design	180	30-Sep-19 A	13-Jan-21
DSA Approval	150	01-Feb-21*	30-Jun-21
Procurement	75	18-Mar-22	31-May-22
Construction	180	01-Jun-22	27-Nov-22
FF&E	30	28-Nov-22	27-Dec-22
Occupy	0		16-Apr-23
Baseball and Softball Facilities	1094	17-Sep-19 A	26-Jul-22
Baseball Field Facilities Upgrades	1014	17-Sep-19 A	26-Jul-22
Programming	180	17-Sep-19 A	30-Apr-20 A
Design	90	18-Jan-21 A	17-Apr-21
DSA Approval	180	18-Apr-21	14-Oct-21
Procurement	90	15-Oct-21	12-Jan-22
Construction	195	13-Jan-22	26-Jul-22
Occupy	0		26-Jul-22
Softball Field Facilities Upgrades	828	17-Sep-19 A	11-Jul-22
Programming	180	17-Sep-19 A	14-Mar-20 A
Design	120	15-Jan-21	17-May-21
DSA Approval	180	18-May-21	13-Nov-21
Procurement	90	14-Nov-21	11-Feb-22
Construction	120	12-Feb-22	11-Jun-22
Occupy	0		11-Jun-22
Landscape Nursery Technology (CMR)	1155	01-Nov-18 A	18-Jan-23
Project Kick-off	0	01-Nov-18 A	
Programming	223	01-Nov-18 A	11-Jun-19 A
Design	320	12-Jun-19 A	24-Aug-20 A
DSA Approval	250	25-Aug-20 A	20-Nov-20 A
Temporary Nursery (Procurement through Construction)	210	09-Dec-20 A	30-Mar-21
Procurement	90	18-Feb-21	18-May-21
Construction	490	19-May-21	20-Sep-22
FF&E	30	21-Sep-22	20-Oct-22
Occupy	0		20-Oct-22
Close-out	90	21-Oct-22	18-Jan-23
Operations and Warehouse Relocation (CMR)	2055	01-Nov-18 A	18-May-23
Project Kick-off	0	01-Nov-18 A	
Programming	180	01-Nov-18 A	29-Apr-19 A
Design	600	30-Apr-19 A	01-Sep-20 A
Increments 1 & 2 (Infrastructure and Grounds)	1145	01-Apr-20 A	22-Nov-22
DSA Approval Increment 1 & 2	100	01-Apr-20 A	02-Nov-20 A
Procurement Increment 1 & 2	60	31-Jan-21	31-Mar-21
Construction Increment 1 & 2	365	03-May-21	02-May-22
Increments 3 & 4 (Main Buildings)	1412	01-Apr-20 A	10-May-24
DSA Approval	120	01-Apr-20 A	20-Oct-20 A
Procurement	60	21-Nov-22	19-Jan-23
Construction Increments 3 & 4	365	20-Jan-23	19-Jan-24
FF&E	30	20-Jan-24	18-Feb-24
Occupy	0		18-Feb-24
Close-out	90	19-Feb-24	18-May-24
IT Data Center (CMR)	1263	04-Aug-19 A	01-Aug-22
Project Kick-off	0	04-Aug-19 A	
Programming	100	05-Aug-19 A	12-Nov-19 A
Design	232	13-Nov-19 A	03-Aug-20 A
DSA Approval	180	04-Aug-20 A	31-Jan-21 A
Procurement	90	01-Feb-21 A	01-May-21
Construction	431	02-May-21	06-Jul-22
Close-out	52	06-Jul-22	29-Jul-22
FF&E	33	30-Jun-22	01-Aug-22
Occupy	0		19-Jul-22
Instructional Building No. 1 and University Center (CMR)	1842	04-Aug-19 A	28-Aug-24
Project Kick-off	0	04-Aug-19 A	
Programming	260	14-Aug-19 A	24-Jul-20 A
Design	365	14-Jul-20 A	21-Aug-21
DSA Approval	180	21-Aug-21	16-Feb-22
Procurement	90	17-Feb-22	17-May-22
Construction	700	31-Jun-22	30-Apr-24
FF&E	30	01-May-24	30-May-24
Occupy	0		30-May-24
Close-out	90	31-May-24	28-Aug-24
Student Union (CMR)	1828	01-Aug-19 A	11-Sep-24
Project Kick-off	0	01-Aug-19 A	
Programming	162	01-Oct-19 A	09-Jun-20 A
Design	400	10-Jun-20 A	24-Jun-21
DSA Approval	180	30-Jul-21	25-Jan-22
Procurement	90	26-Jan-22	25-Apr-22
Construction	750	26-Apr-22	14-May-24
FF&E	30	15-May-24	13-Jun-24
Occupy	0		13-Jun-24
Close-out	90	14-Jun-24	11-Sep-24

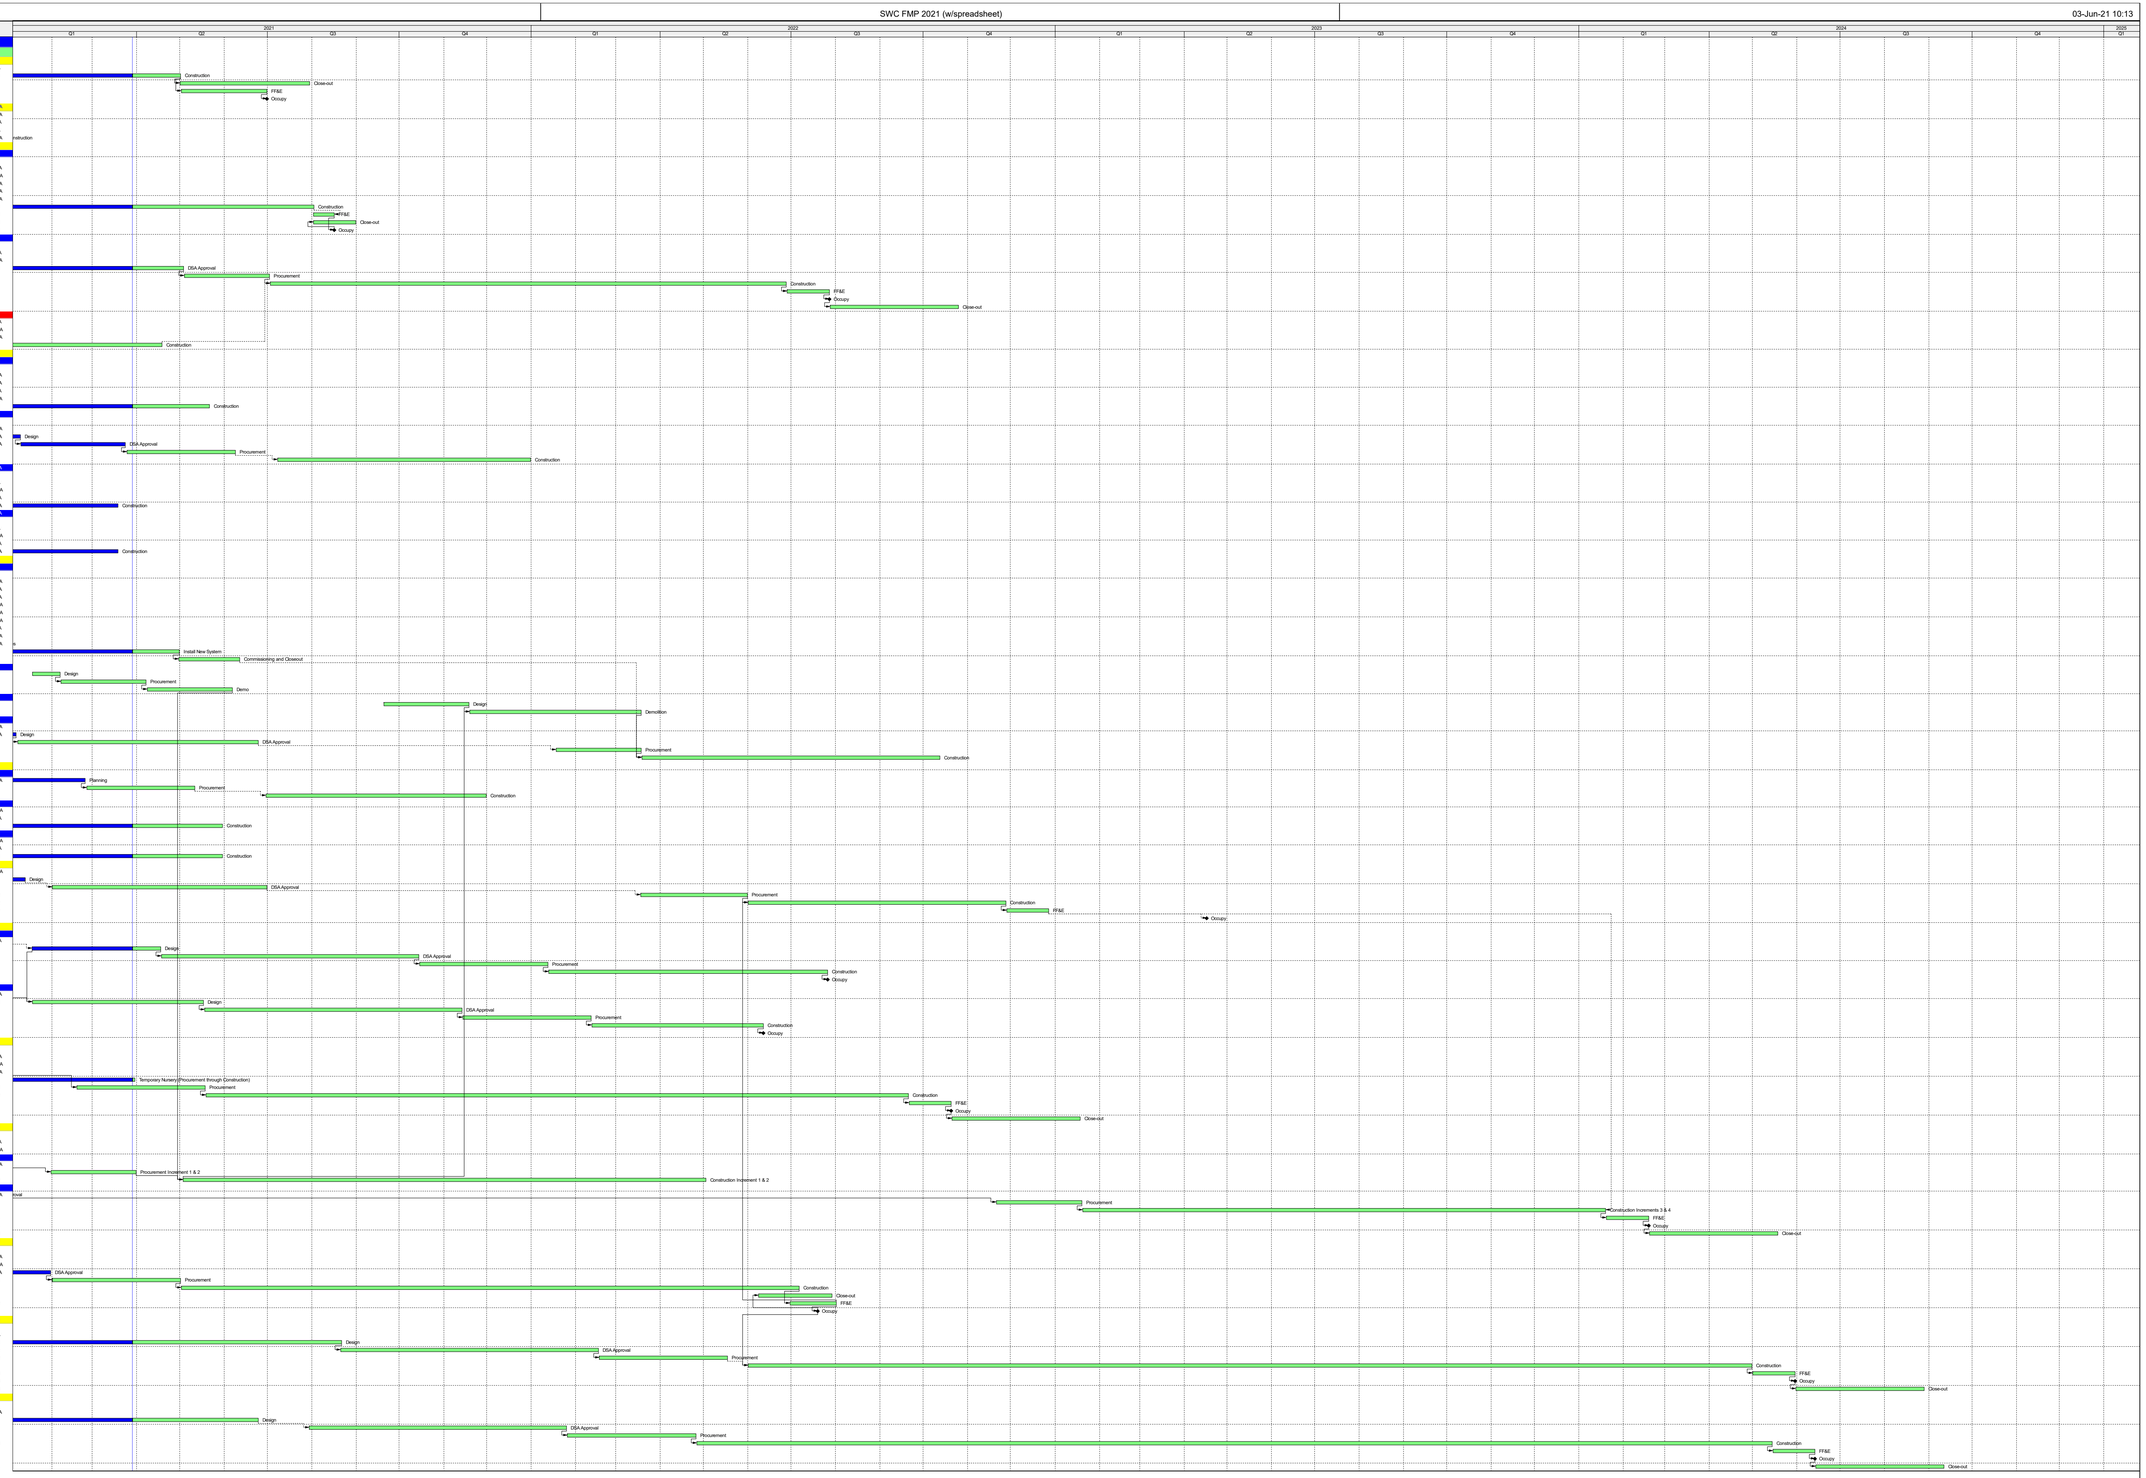

Actual Work | Critical Remaining Work | Remaining Work | Milestone
