SWC 2018 FVP Schedule

Proposition R & Z

July 2022 Update

August upate being prepared to be posted in September.

Activity ID	Activity Name	Remaining Duration	Start	Finish
Southwestern Community College District		947	03-Sep-18 A	31-Jan-25
Phase 1 Projects		947	03-Sep-18 A	31-Jan-25
Student Union		918	10-Aug-20 A	31-Jan-25
1A	Planning	0	10-Aug-20 A	01-Mar-21 A
1B	Project Programing	0	02-Mar-21 A	11-Jun-21 A
2A	Design	0	14-Jun-21 A	26-Aug-21 A
2C	DSA	0	02-Aug-21 A	28-Feb-22 A
3A	Bid	0	11-May-22 A	28-Jun-22 A
4A	Award	0	29-Jun-22 A	09-Aug-22 A
5A	Construction	795	10-Aug-22 A	30-Sep-24
5C	Substantial Completion	0		30-Sep-24
5D	FF&E	52	01-Oct-24	21-Nov-24
5E	Move Users In	5	17-Nov-24	21-Nov-24
6A	Close Out	93	31-Oct-24	31-Jan-25
Baseball & Softball Upgrades		211	17-Sep-19 A	10-Apr-23
1A	Planning	0	17-Sep-19 A	17-Sep-19 A
1B	Project Programing	0	17-Sep-19 A	01-Aug-21 A
2A	Design	0	18-Jun-21 A	28-Nov-21 A
2C	DSA	0	21-Aug-21 A	06-May-22 A
3A	Bid	44	12-Sep-22*	25-Oct-22
4A	Award	0	26-Oct-22	26-Oct-22
5A	Construction	137	26-Oct-22	11-Mar-23
5C	Substantial Completion	0		11-Mar-23
6A	Close Out	30	12-Mar-23	10-Apr-23
Mayan Hall Demolition		60	03-Jan-20 A	24-Oct-22
1A	Planning	0	02-Jan-20 A	13-Apr-20 A
2A	Design	0	14-May-20 A	13-Jan-21 A
2C	DSA	0	15-Nov-20 A	26-Oct-21 A
3A	Bid	0	01-Aug-21 A	20-Sep-21 A
4A	Award	0	20-Sep-21 A	26-Oct-21 A
5A	Construction	0	06-Dec-21 A	15-Aug-22 A
5C	Substantial Completion	0		15-Aug-22 A
6A	Close Out	60	26-Aug-22	24-Oct-22
Campus-Wide Trellis Repairs		309	01-Nov-21 A	24-May-23
1A	Planning	0	01-Nov-21 A	15-Nov-21 A
1B	Project Programing	0	16-Nov-21 A	30-Nov-21 A
2A	Design	0	01-Dec-21 A	03-Feb-22 A
2C	DSA	70	14-Feb-22 A	06-Oct-22
3A	Bid	60	07-Oct-22	05-Dec-22
4A	Award	10	06-Dec-22	15-Dec-22
5A	Construction	130	16-Dec-22	24-Apr-23
5C	Substantial Completion	0		24-Apr-23
6A	Close Out	30	25-Apr-23	24-May-23
Fire Alarm Upgrades		150	06-Jan-20 A	25-Dec-22
1A	Planning	0	06-Jan-20 A	23-Mar-20 A
1B	Project Programing	0	23-Mar-20 A	31-Mar-20 A
2A	Design	0	01-Apr-20 A	08-Oct-20 A
2C	DSA	0	01-Jul-20 A	01-Aug-21 A
3A	Bid	0	19-Oct-20 A	08-Dec-20 A
5A	Construction	150	09-Dec-20 A	25-Dec-22
6A	Close Out	30	22-Oct-22	20-Nov-22
Ceramic Relocation		92	02-Jan-20 A	29-Sep-22
1A	Planning	0	02-Jan-20 A	01-Aug-20 A
1B	Project Programing	0	02-Aug-20 A	02-Sep-20 A
2A	Design	0	03-Sep-20 A	01-Aug-21 A
3A	Bid	0	04-Sep-20 A	01-Aug-21 A
5A	Construction	72	14-Oct-20 A	09-Sep-22
6A	Close Out	20	10-Sep-22	29-Sep-22
Sewer Line and Path of Travel		113	22-Apr-20 A	21-Oct-22
1A	Planning	0	22-Apr-20 A	02-Nov-20 A
1B	Project Programing	0	22-Jun-20 A	02-Nov-20 A
2A	Design	0	03-Nov-20 A	24-Mar-21 A
2C	DSA	0	10-Jan-21 A	01-Aug-21 A
3A	Bid	0	25-Mar-22 A	29-Apr-22 A
4A	Award	0		29-Apr-22 A
5A	Construction	113	31-May-22 A	20-Oct-22
5C	Substantial Completion	0		20-Oct-22
6A	Close Out	0	21-Oct-22	21-Oct-22
Tennis Courts		466	01-Sep-19 A	15-Feb-24
1A	Planning	0	01-Sep-19 A	08-Nov-19 A
1B	Project Programing	0	11-Nov-19 A	30-Dec-19 A
2A	Design	0	31-Dec-19 A	10-Nov-21 A
2C	DSA	0	11-Nov-21 A	13-May-22 A
3A	Bid	60	07-Nov-22*	05-Jan-23
4A	Award	20	06-Jan-23	25-Jan-23
5A	Construction	208	26-Jan-23	21-Aug-23
6A	Close Out	178	22-Aug-23	15-Feb-24
Instructional Complex #1		811	04-Aug-20 A	01-Oct-24
1A	Planning	0	04-Aug-20 A	01-Feb-21 A
1B	Project Programing	0	02-Feb-21 A	25-May-21 A
2A	Design	0	02-Nov-21 A	02-May-22 A
2C	DSA	27	30-Mar-22 A	09-Aug-22
3A	Bid	0	19-Apr-22 A	17-May-22 A
4A	Award (includes CBA Alignment)	0	18-May-22 A	11-Jul-22 A
5A	Construction	763	20-Jul-22 A	14-Aug-24
5C	Substantial Completion	0		14-Aug-24
5D	FF&E	28	15-Aug-24	11-Sep-24
5E	Move Users In	20	12-Sep-24	01-Oct-24
6A	Close Out	35	15-Aug-24	18-Sep-24
Landscape + Nursery Technology		846	01-Nov-18 A	29-Dec-24
1A	Planning	0	01-Nov-18 A	11-Jan-19 A
1B	Project Programing	0	01-Nov-18 A	11-Jan-19 A
2A	Design	0	11-Jan-19 A	24-May-22 A
2C	DSA	0	01-Jul-22 A	11-Jul-22 A
3A	Bid #3	60	06-Sep-22*	04-Nov-22
4A	Award	20	05-Nov-22	24-Nov-22
5A	Construction	426	25-Nov-22	24-Jan-24
5C	Substantial Completion	0		24-Jan-24
5D	FF&E	120	25-Jan-24	23-May-24
5E	Move Users In	10	24-May-24	02-Jun-24
6A	Close Out	210	03-Jun-24	29-Dec-24
Building 710 Electrical Relocation		60	05-Aug-19 A	28-Aug-22
1A	Planning	0	02-Jan-20 A	13-Oct-20 A
1B	Project Programing	0	02-Jan-20 A	01-Aug-21 A
2A	Design	0	05-Aug-19 A	02-Oct-20 A
5A	Construction	0	13-Oct-20 A	28-Jul-22 A
6A	Close Out	60	05-Jul-22 A	28-Aug-22
Jaguar Village		92	03-Sep-18 A	28-Oct-22
1A	Planning	0	03-Sep-18 A	13-Nov-19 A
1B	Project Programing	0	13-Nov-19 A	06-Dec-19 A
2A	Design	0	09-Dec-19 A	31-Jan-20 A
2C	DSA	0	02-Aug-21 A	28-Sep-21 A
3A	Bid	0	15-Dec-21 A	19-Jan-22 A
4A	Award	0		19-Jan-22 A
5A	Construction	62	23-Feb-22 A	28-Sep-22
5C	Substantial Completion	0		28-Sep-22
6A	Close Out	30	29-Sep-22	28-Oct-22
IT Data Center		60	02-Aug-19 A	28-Sep-22
1A	Planning	0	04-Aug-19 A	12-Nov-19 A
1B	Project Programing	0	02-Aug-19 A	05-Aug-19 A
2A	Design	0	05-Aug-19 A	03-Aug-20 A
2C	DSA	0	03-Aug-20 A	31-Jan-21 A
3A	Bid	0	31-Jan-21 A	19-Jul-21 A
4A	Award	0	20-Jul-21 A	20-Jul-21 A
5A	Construction	0	21-Jul-21 A	22-Jul-22 A
5C	Substantial Completion	0		22-Jul-22 A
5D	FF&E	0	01-Aug-22 A	05-Aug-22 A
5E	Move Users In	0	08-Aug-22 A	12-Aug-22 A
6A	Close Out	60	15-Aug-22 A	28-Sep-22
Operations and Warehouse Relocation		163	01-Nov-18 A	10-Jan-23
1A	Planning	0	01-Nov-18 A	28-Dec-18 A
1B	Project Programing	0	02-Jan-19 A	13-Jun-19 A
2A	Design	0	14-Mar-19 A	02-Jul-20 A
2C	DSA	0	29-Aug-19 A	02-Jul-20 A
3A	Bid	0	01-Mar-21 A	15-Jun-21 A
4A	Award	0	23-Aug-21 A	23-Aug-21 A
5A -1	Construction Increment 1	152	26-Aug-21 A	30-Dec-22
5A -2	Construction Increment 2	115	23-Aug-21 A	23-Nov-22
5C	Substantial Completion	0		30-Dec-22
5D	FF&E	60	01-Nov-22	30-Dec-22
6A	Close Out	60	12-Nov-22	10-Jan-23

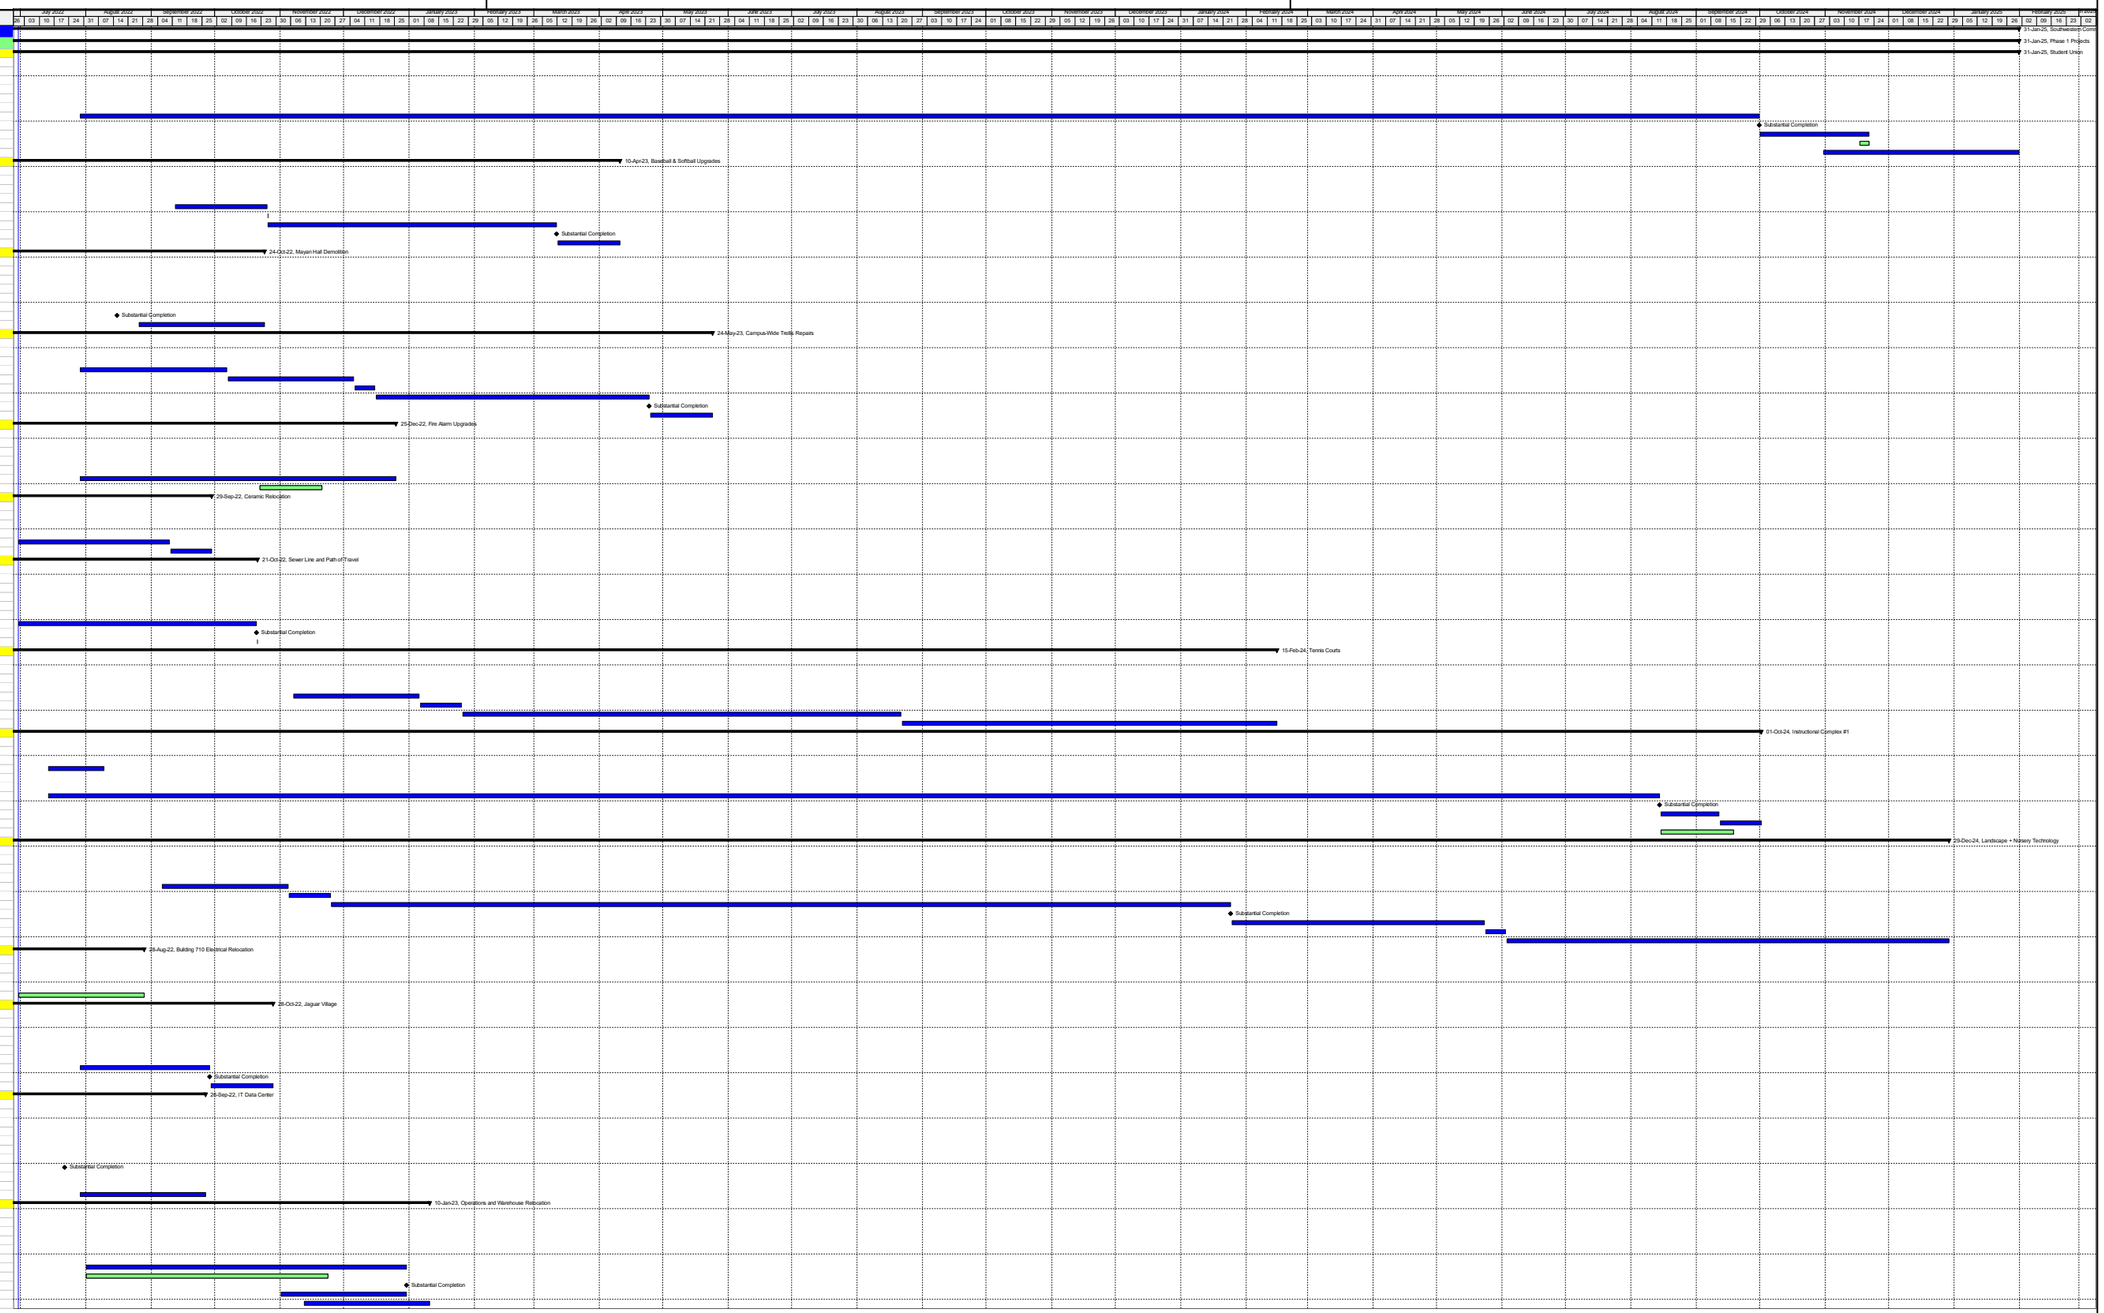

Actual Work ◆ Milestone

Remaining Work Summary

Schedular: Mike Carmichael - mcarmichael@swccd.edu
